

FIFTH BIENNIAL REPORT

OF THE

Board of Capitol Managers

TO THE


GENERAL ASSEMBLY

OF THE

STATE OF COLORADO.



1892.

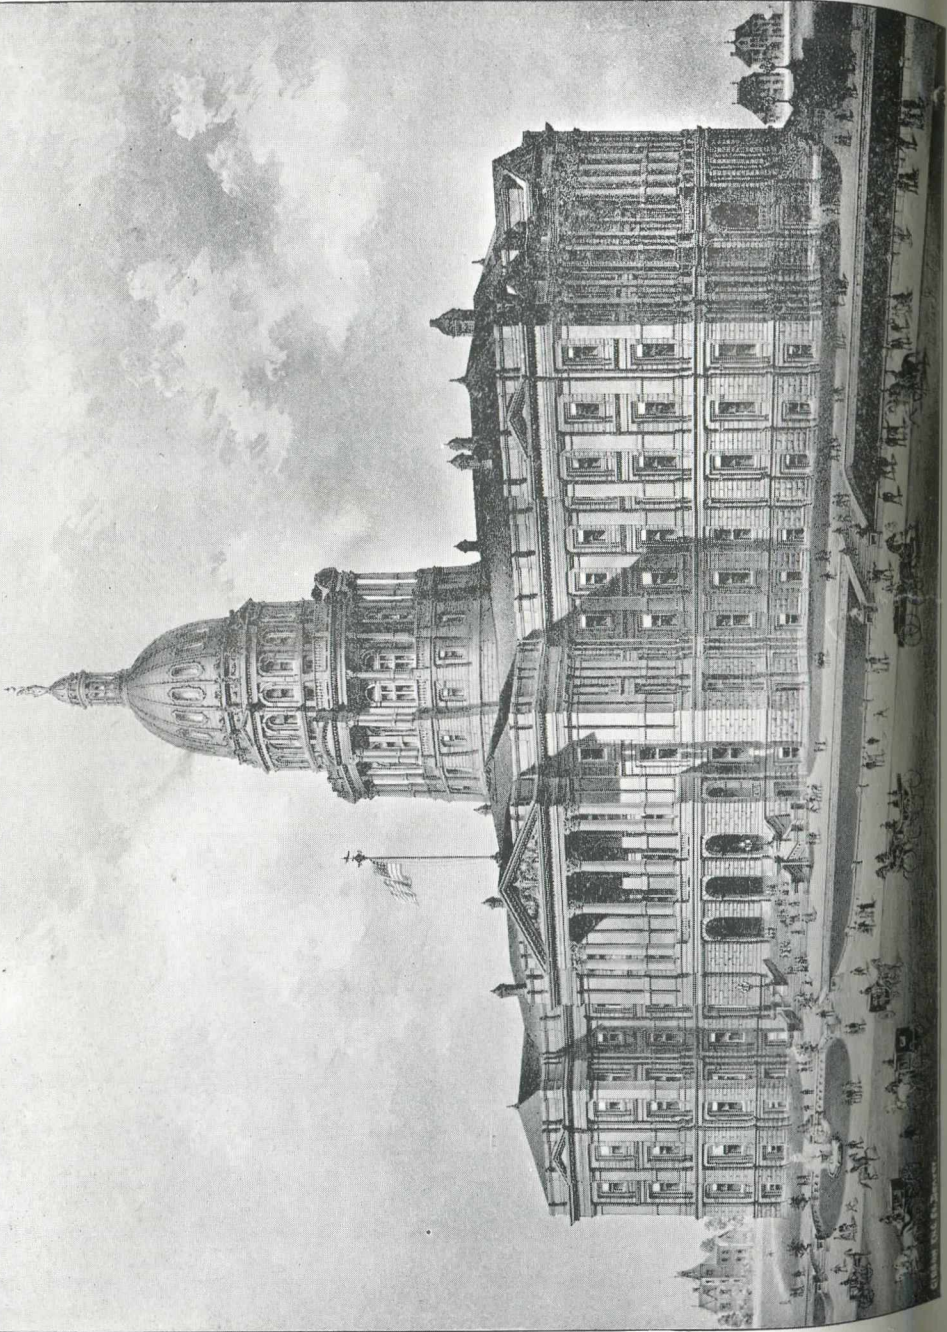

COLORADO STATE CAPITOL BUILDING, DENVER.

FIFTH BIENNIAL REPORT
OF THE
BOARD OF CAPITOL MANAGERS
TO THE
GENERAL ASSEMBLY
OF THE
STATE OF COLORADO.

DECEMBER 1, 1892.

COLORADO SPRINGS, COLO.
THE GAZETTE PRINTING COMPANY, STATE PRINTERS.
1892.

STATE OF COLORADO. }
OFFICE OF THE BOARD OF CAPITOL MANAGERS, }
DENVER, COLO., December 1, 1892. }

To His Excellency,

JOHN L. ROUTT,

Governor of the State of Colorado:

SIR—We have the honor to submit for your consideration the Fifth Biennial Report of the Board of Capitol Managers, to be laid before the next General Assembly.

Respectfully,

JOB A. COOPER,

OTTO MEARS,

BENJAMIN F. CROWELL,

CHARLES J. HUGHES, JR.,

Managers.

BOARD OF CAPITOL MANAGERS.

JOHN L. ROUTH,
Governor and Ex-officio Chairman.

JOB A. COOPER.

OTTO MEARS.

BENJAMIN F. CROWELL.

CHARLES J. HUGHES, JR.

HERMAN LUEDERS *Secretary.*

PETER GUMRY *Superintendent.*

THOMAS MULLEN *Assistant Superintendent.*

CONTRACTORS.

GEDDIS & SEERIE.

LANE BRIDGE AND IRON WORKS.

THE COLORADO IRON WORKS.

FREDERICK STAPP.

FRANK ANDERSON.

REPORT

OF THE

BOARD OF CAPITOL MANAGERS

OF THE

STATE OF COLORADO.

DENVER, COLO., December 1, 1892.

To the General Assembly of the State of Colorado:

In accordance with the provisions of an act of the General Assembly of the State of Colorado, entitled "An act to provide for the erection and completion of a State Capitol building, at the City of Denver, and creating a Board of Management and Supervision," approved April 1st, 1889, we herewith respectfully present the following report of our transactions for the years A. D. 1891 and 1892.

The election of Manager John L. Routh as Governor of Colorado, and the assumption by him of the duties of that office in January, 1891, created a vacancy in the membership of the Board, which was filled by the appointment of ex-Governor Job A. Cooper.

The following is a synopsis of the important business transacted by the Board outside of the routine affairs.

SUPERVISING ARCHITECT.

At a meeting held December 15th, 1890, the question arose as to the necessity for employing a supervising architect, the duties of such having been performed, since the discharge of E. E. Myers, late Supervising Architect, June, 1889, by Peter

Gumry, Superintendent, thereby saving the State a large amount for commission, traveling expenses, etc.

The Board being in doubt about the matter, Mr. Charles J. Hughes, Jr., was requested to prepare a legal opinion, which was, in substance, as follows:

That by the terms of the contract with Geddis & Seerie, the Board was bound to have a superintendent, but was not bound to provide an architect; that the Board could put upon the Superintendent duties in addition to those put upon him by the provisions of the contract itself; that if the Board made changes, and the contractors consented to them, the approval of the architect was unnecessary; and that, so far as the legality of the action of the Board, under the contract, is concerned, they are not affected by the failure to provide an architect.

In view of the foregoing, the Board has not employed a supervising architect, but all the duties incident to this office have been performed by Mr. Peter Gumry, Superintendent, without additional compensation.

W. D. RICHARDSON LABOR RELIEF.

In accordance with an act of the last General Assembly, approved April 11, 1891, providing for the relief of certain laborers who had performed work on the Capitol building and in the granite quarries at Georgetown, for W. D. Richardson, during the year 1877, formerly contractor for the erection of the said Capitol building, and who had not been paid for their labor, on account of the failure of said Richardson to comply with his contract, and his insolvency, and appropriating \$5,000 for the above purpose out of the Capitol building fund, and authorizing the Board of Capitol Managers to audit such claims, it was discovered that said work had been performed during the year 1887 and not, as the act stated, in 1877. The Attorney General having filed his opinion upon

this question, to the effect that the presence of the date, 1877, in said act was a mistake, which should be corrected by construing the law to mean 1887, the Board, on October 3d, 1891, adopted the following regulations to govern the auditing of these claims:

That every person making claim should file with the Secretary of the Board a sworn claim, setting forth the name and residence, the character of work performed, the term when the same was performed, for whom the same was performed, the number of days he was engaged in said labor, the compensation per day he was to receive, the total amount of said claim, the amount he had received in payment thereon, if anything; and that he had not assigned or otherwise disposed of said claim, but was the present holder thereof. Or, if said claim be made by a person claiming as assignee from a laborer, the fact should be stated and the written assignment of the same should be filed with the claim. In addition to the sworn claim filed, claimants should file their time checks or other evidence of indebtedness issued to them on behalf of Richardson.

For claims allowed, claimants should receipt to the Board, giving their voucher for the same, and assigning and transferring to the Board their claims against W. D. Richardson for the amount of the allowance.

The following notice was published in the Denver newspapers for ten days, notifying parties to file their claims:

Any persons having claims for compensation as laborers upon the Capitol building at Denver and in the granite quarries at Georgetown, against W. D. Richardson, contractor, during the year 1887, may file a written claim, under oath, for the same with the Secretary of the Board of Capitol Managers, at any time within sixty days from the 5th day of October, A. D. 1891.

Requirements of proof can be found at the office of the Board, Room 44, Barclay Block.

By order of the Board.

HERMAN LUEDERS, *Secretary.*

There being nothing on record in this office to guide the Board as to the validity of the claims presented, it was a fortunate circumstance that through the courtesy of Messrs.

Thomas & Thomas, attorneys, they obtained a time book giving the names, services, etc., of employes, during September and October, 1887.

Up to date, ninety-six claims have been examined, of which ninety-three were allowed and three were rejected. The latter are:

King & France, hauling material.....	\$1,345 53
Albert Schulz, general superintendent.....	325 00
T. A. Jackson, clerk.....	150 00

As far as can be ascertained, there is a record of \$800 worth of labor performed, for which no claimants have appeared, and a balance on hand, of the original appropriation, of \$814.23.

It may be presumed that but few of the remaining claims will ever be presented, owing to the fact that the claimants have long since removed from the State.

E. E. MYERS,

LATE ARCHITECT OF THE CAPITOL BUILDING.

June 3d, 1891, the Board passed a resolution instructing the Secretary to notify Mr. Myers that the amount of \$1,600 was at his disposal, as soon as he could show a satisfactory adjustment of all assignments and attachments against him, thereby relieving the State from all further liability in this matter.

This action was taken at the suggestion of the chairman, and with a view of arranging a settlement with Mr. Myers, owing to the numerous written requests received from him by the several members of the Board, but no reply was made.

August 30th, 1892, Mr. Charles Mills addressed the Board regarding his late father's claim against Mr. Myers, amounting to \$1,737. He was informed that the Board would not hesitate to settle this matter, as far as the amount due E. E. Myers was concerned, namely, \$1,600, in full of all demands against the State, providing he would conform with the terms of the above resolution.

The following communication was read by the Secretary, October 5th, 1892:

DETROIT, MICH., September 20, 1892.

The Board of Capitol Managers of the State of Colorado.

GENTLEMEN—You will please take notice that a certain assignment made by me to William B. Mills, late of Denver, of my claim against the State of Colorado, under contract with yourselves, for the superintending of the building of the State capitol, was made by me at the request of said Mills, and merely for the purpose of securing him for services performed and to be performed by him as attorney in my behalf, and to facilitate him in the collection of said claim, and that said assignment was not intended as an absolute assignment of the whole amount of said claim.

You will, therefore, please make no settlement, with any person, of said claim without my consent in writing thereto.

Yours etc.,

E. E. MYERS.

CAPITOL BUILDING GROUNDS.

As soon as the use of the grounds by the contractors ceased to be necessary, the fence and houses were removed, and on April 6th, 1892, the Board entered into an agreement with Mr. Geo. H. Angell, C. E., to make a survey, taking elevations every ten feet each way, prepare a plat, estimate the amount of earth necessary to be removed, and establish proper grades. May 4th, Mr. Angell presented his report, estimating that in order to grade the grounds from west front to Broadway, 13,500 yards of earth would have to be moved.

On May 22d, the Board assembled to open proposals for grading the grounds, received in response to an advertisement published for ten days in the three Denver dailies, which were as follows:

No. 1. William Ford.....	\$1,675 00
No. 2. G. W. Harriman.....	1,600 00
No. 3. J. A. Osner.....	1,275 00
No. 4. T. C. Scanlon.....	1,143 00
No. 5. John Kiely.....	1,505 ⁰⁰
No. 6. B. A. Harbour & Co.....	1,300 00
No. 7. J. P. McAdams.....	1,324 00
No. 8. Geddis & Seerie.....	1,260 00
No. 9. Wellet & Co.....	1,650 00

Mr. T. C. Scanlon being the lowest bidder, he was awarded the contract, for \$1,143.

As soon as a room in the Capitol building can be prepared for the Superintendent's office, the building heretofore occupied for that purpose, on Colfax avenue, will be removed.

The Committee on Grounds is now engaged in finishing grading around the Capitol on Colfax avenue and Fourteenth avenue, and a space for a sidewalk around the entire grounds, 30 feet in width, will be left.

In order to obtain a proper grade for terracing and reducing the elevation of the ground, it was necessary to lower the west approach, or main entrance of the building, two feet below the former level.

To comply with the law, a regular system of water closets had to be constructed.

It is a matter of regret to the Board not to have been able to comply with the numerous requests of prominent citizens to beautify the grounds for the conclave. To do this would have required the expenditure of considerable money, which the Board was not justified in taking from the appropriation authorizing them to lay out, ornament, and beautify the grounds, as the improvement for the conclave could only have been of a temporary character, and the amount expended therefor wasted. Whatever plan to ornament the grounds may be finally adopted, the work performed so far would have necessarily to be done anyhow.

CONTRACTS.

IRON WORK IN ATTIC FLOOR, ROOF AND ROOF CONSTRUCTION, AND PART OF DOME.

On May 14th, 1891, the Board advertised for proposals in the Denver Republican, Denver Times, Rocky Mountain News, Colorado Sun, Engineering News, and Engineering Record, New York City.

May 29th, the Board extended the time for receiving proposals from June 6th until June 16th, on which latter day the bids were opened and ordered tabulated.

June 17th, the Secretary read the following statement of the proposals:

<i>CLASS No. 1—Steel and wrought iron work, complete.</i>	
The Pittsburgh Bridge Company, Pittsburgh.....	\$79,677 00
Lane Bridge and Iron Works, Chicago.....	68,675 00
The Stewart Iron Works, Wichita.....	86,890 00
<i>CLASS No. 2—Cast iron work, complete.</i>	
The Stewart Iron Works, Wichita.....	9,884 00
<i>CLASS No. 3—Tanks in place, complete.</i>	
Frederick Stapp, Denver.....	1,095 00
The Stewart Iron Works, Wichita.....	1,500 00
<i>CLASS No. 4—Slate and slate work, complete.</i>	
E. M. Dodd, Denver.....	20,560 00
Grygla & Selden, Minneapolis.....	16,770 00
Frederick Stapp, Denver.....	18,443 00
W. H. Mullin, Salem, Ohio—	
<i>Washington Slate:</i>	
Sample 1, asbestos sheathing, 5-inch lap.....	17,582 64
Sample 2, fire and water proof sheathing, 5-inch lap.	18,422 55
<i>Peach Bottom Slate:</i>	
Sample 1, asbestos sheathing, 5-inch lap.....	23,150 52
Sample 2, fire and water proof sheathing, 5-inch lap.	23,970 00
<i>Old Bangor:</i>	
Sample 1, asbestos sheathing, 5-inch lap.....	27,217 05
Sample 2, fire and water proof sheathing, 5-inch lap.	28,056 84
<i>CLASS No. 5—Galvanized iron and copper work, complete.</i>	
Fred. Stapp, Denver.....	4,855 00
E. M. Dodd, Denver.....	8,551 00
W. H. Mullins, Salem, Ohio.....	8,967 41
<i>CLASS No. 6—Skylight in roof, complete.</i>	
Fred. Stapp, Denver.....	1,763 00
W. H. Mullins, Salem, Ohio.....	1,587 50
<i>CLASS No. 7—Carpenter work, complete.</i>	
Des Jardins & Handy, Denver.....	9,859 00
Francis Callahan, Denver.....	8,450 00
A. S. Ripley & Son, Denver.....	7,900 00
The Hallack-Sayre-Newton Lumber Company, Denver..	6,860 00
Frank Anderson, Denver.....	6,100 00

CLASS NOS. 1 AND 2— <i>Steel, wrought and cast iron work.</i>	
Lane Bridge and Iron Company, Chicago.....	\$76,774 00
CLASS NOS. 1 AND 3— <i>Steel and wrought iron work; tanks in place.</i>	
Lane Bridge and Iron Works.....	69,875 00
CLASS NOS. 1, 2 AND 3— <i>Steel, wrought and cast iron work; tanks in place.</i>	
Lane Bridge and Iron Works.....	77,975 00
CLASS NOS. 4, 5 AND 6— <i>Slate and slate work, galvanized iron and copper work, skylight in roof.</i>	
James A. Miller & Bro., Chicago.....	38,877 00
Grygla & Selden, Minneapolis.....	27,900 00
C. B. Fair, Denver.....	26,055 00
CLASS NOS. 5 AND 6— <i>Skylight and carpenter work.</i>	
Grygla & Selden, Minneapolis.....	11,675 00
CLASS NOS. 1 TO 6— <i>Carpenter work excluded.</i>	
Lane Bridge and Iron Works, Chicago.....	116,851 00
CLASS NOS. 1 TO 7—	
Geddis & Seerie, Denver.....	124,000 00

Mr. Mullins also quoted figures on slate with 3-inch lap, but the specifications calling for 5-inch lap, his figures could not be considered. He also stipulated that he would only contract for Classes 4, 5 and 6, or none.

After considering the bids, the Board resolved to award Classes 1, 2 and 3 to one party; likewise Classes 4, 5 and 6; likewise Class 7.

The following bids, having been found to be the lowest, were accepted, and distributed as follows:

Lane Bridge and Iron Works, Chicago:	
Classes 1, 2 and 3.....	\$77,975 00
Frederick Stapp, Denver:	
Classes 4, 5 and 6.....	25,061 00
Frank Anderson, Denver:	
Class 7.....	6,100 00
Total amount.....	\$109,136 00

ROOF DRAINAGE SYSTEM.

At a meeting of the Board, on December 10, 1891, bids were received for the roof-drainage system, as per advertisement published for fifteen days in the Denver Times, Denver Republican, Rocky Mountain News, and Colorado Sun. The bids were:

No. 1. Geddis & Seerie.....	\$2,000 00
No. 2. Hughes & Keith Sanitary Supply Co.....	2,100 00

The bid of the former firm was accepted.

TEMPORARY ENCLOSING THE BUILDING.

On August 30, 1892, the Board passed a resolution to temporarily close the doors and windows, as a protection to the building, to remain until the plastering was finished, and instructed the Secretary to advertise for ten days, for bids, in the Denver Republican, Colorado Sun, and Rocky Mountain News. Five proposals were received, namely:

No. 1. J. S. Buell.....	\$1,725 60
No. 2. J. W. Hudson.....	1,399 80
No. 3. George Scott.....	2,439 80
No. 4. Charles Dillon.....	1,727 70
No. 5. Frank Anderson.....	1,314 05

Mr. Anderson being the lowest bidder, he was awarded the contract at the amount stated.

EXTERIOR CONSTRUCTION OF DOME.

August 30, 1892, the Superintendent submitted fifty-two detail drawings, showing the exterior finish of the dome, except the figure surmounting the same, which were examined and approved. The Secretary was authorized to prepare and submit a form of advertisement calling for proposals, classifying material and labor, as follows:

CLASS 1. Cast and wrought iron work, complete.

CLASS 2. Copper and galvanized iron work, complete.

CLASS 3. Corrugated iron work, as much as may be required.

CLASS 4. Painting, sanding, glazing, and carpenter work, complete.

CLASS 5. Terra cotta work, or wire lath and cement work, as much as may be required.

This advertisement was published for thirty days in the Denver Republican, Colorado Sun, Engineering Record (New York), and Engineering Publishing News Company (New York).

The bids received were opened November 9th, and the Secretary ordered to prepare a tabulated statement, which was presented at an adjourned meeting, held November 11th, and read as follows:

CLASS No. 1—*Cast and wrought iron work complete.*

Lane Bridge and Iron Works, Chicago.....	\$79,850 00
Chicago Ornamental Iron Co., Chicago.....	84,300 00
The Davis-Creswell Manufacturing Co., Denver.....	82,970 00
The Winslow Bros. Co., Chicago, (cast iron only).....	55,750 00

CLASS No. 2—*Copper and galvanized iron work, complete.*

Lane Bridge and Iron Works.....	7,800 00
Fred. Stapp, Denver.....	9,545 00

CLASS No. 3—*Corrugated iron work, as much as may be required.*

Lane Bridge and Iron Works, per square foot.....	15
--	----

CLASS No. 4—*Painting, sanding, glazing and carpenter work.*

Lane Bridge and Iron Works.....	9,300 00
Frank Anderson, Denver.....	6,863 28

CLASS No. 5—*Terra cotta.*

Lane Bridge and Iron Works.....	1,900 00
---------------------------------	----------

CLASS No. 5—*Cement and wire lath, in lieu of terra cotta.*

Lane Bridge and Iron Works.....	1,550 00
---------------------------------	----------

The proposal of The Winslow Brothers Company not being in accordance with the terms of the advertisement, it was not considered.

After due consideration, the following action was taken:

Class No. 1, awarded to Lane Bridge and Iron Works, at \$79,850.

Class No. 2, awarded to Lane Bridge and Iron Works, at \$7,800.

Class No. 3, rejected.

Class No. 4, awarded to Frank Anderson, at \$6,863.28.

Class No. 5, rejected.

Proposals for Classes No. 3 and 5 to be re-advertised.

CAPITOL BUILDING BONDS.

The Board of Commissioners of the State Debt convened at the Governor's office, December 9th, 1891, in accordance with an act of the Eighth General Assembly, entitled "An act to provide for the creation of an additional bonded indebtedness by the State, to the amount of three hundred thousand dollars, to aid in the construction of the State Capitol building," approved March 26th, 1891. (P. 49, Session Laws of 1891.)

Present:

Hon. John L. Routt, *Governor*;

Hon. Edwin J. Eaton, *Secretary of State*;

Hon. John M. Henderson, *Auditor of State*.

December 28th, 1891, the Board met to consider the following proposals, received in response to advertisements published in the Denver Republican, Colorado Sun, Rocky Mountain News, Denver Times, and the Commercial and Financial Chronicle, of New York:

Bid No. 1—Blair & Co., offering \$307,860 for the entire issue of the second series of Capitol Building bonds, subject, however, to the condition that these bonds must be a legal investment for the Savings Bank of New York State.

Bid No. 2—N. W. Harris, offering \$133 premium for the entire issue.

Bid No. 3—H. Leopold, offering \$303,750 for the entire issue.

Bid No. 4—McIntosh & Mygatt, offering \$300,560 for the entire issue.

Bid No. 5—Geo. H. Taylor, offering \$301,125 for the entire issue.

By unanimous vote of the Board, the bid of H. Leopold, at \$303,750, was accepted.

The entire bonded indebtedness of the State of Colorado now consists of Capitol Building bonds, first and second series; total, six hundred thousand dollars.

INTEREST ON CAPITOL BUILDING BONDS.

In accordance with Section 7 of the acts of 1883 and 1889, providing for the creation of a bonded indebtedness by the State to the amount of \$300,000 and \$300,000, respectively, to

aid in the construction of the State Capitol building, the State Treasurer was authorized and directed to apply any moneys at that time in his hands belonging to the Capitol building fund, for the payment of coupons representing the first year's interest accruing on the bonds to be issued under said acts, such moneys so used to be restored by him to the said Capitol building fund by transfer from the Interest fund as soon as a sufficient amount was received into the said Interest fund from the collection of interest tax, as provided by law.

During the last two years, there has been taken and applied by the State Treasurer, from the Capitol building fund, \$13,875 in payment of the coupons representing the interest on first and second series up to the close of the present fiscal year. For this amount, the Secretary has no vouchers, as the State Treasurer has paid this sum from the Capitol building fund. It appears, however, that Auditor Schwanbeck issued his warrant, for the payment of part of the amount above mentioned, to Treasurer Brisbane, being \$2,625, but no warrants were issued for the balance of interest paid during the term of Auditor Henderson and Treasurer Carlile.

The Auditor's balance of Capitol building fund should show a difference of appropriation unexpended of \$11,250.

The Secretary has opened an account named "Capitol Building Interest," showing a debit of \$13,875 to be repaid to the Capitol building fund as soon as the Treasurer has sufficient amount on hand collected for Interest fund.

CHANGES IN WORK, AND ADDITIONS.

As the granite and brick-work progressed, the Board saw itself confronted with the absolute necessity for making certain changes and additions. Owing to defects in the original plans, drawings and specifications, the Superintendent found himself embarrassed by obstacles which would not permit certain parts of the work to be carried out as designed by the

architect, and which could only be overcome by adopting the following changes:

1. Alterations from straight lintels to semi-circle of window-heads under east portico.

The original designs, by the architect, of the approach under the east portico were for narrow steps, with door-heads semi-circles, and straight lintels for windows. In consequence of the widening of the steps, it became necessary to change the lintels of the windows to semi-circles, in order to harmonize with the door-heads.

2. Fluting pilaster caps.

On the scale-drawing furnished by the architect at the time the work was estimated, the pilaster caps were to be of plain finish. After the contract had been let, full detail drawings were furnished by the architect, showing the pilaster caps with fluted necks, which, after due deliberation, was concluded to be the proper style of finish.

3. Carving Corinthian caps.

The original plans furnished by Architect Myers called for plain caps for the twenty columns supporting the pediments over the entrances, finished in the same style as the pilaster caps. The perspective drawings of the elevation, likewise furnished by the architect, show these columns with Corinthian caps, which he undoubtedly considered the proper style of architecture. The Board therefore concluded that to enhance the exterior beauty of the building, this additional change should be made.

4. Adding four steps to main entrance at west front.

In view of the fact that the approach to the main entrance at the west front was lowered two feet (see capitol building grounds), it became necessary to add four steps with railings, and additional masonry.

5. Changing spandrels of all outside steps from rock-face to six-cut.

Although the original specifications, drawings and elevations called for rock-face, it was decided to change this work to six-cut, in order to harmonize with the exterior finish of the building.

6. Changing cut-stone work of dentil course in main cornice from sunk V bevel to sunk space.

The original drawings by Architect Myers, to a scale of $\frac{1}{2}$ inch and $1\frac{1}{2}$ inches to the foot, show a sunk V bevel, and upon these drawings and details Messrs. Geddis & Seerie based their calculations. After the contract had been awarded, the architect furnished a full-size detail drawing, showing the dentil course with a sunk space 4 inches by 5 inches by $10\frac{1}{2}$ inches, in place of the sunk V bevel, the latter being correct. It therefore became necessary to adopt this change as designed by the architect in the full-size detail drawings.

7. Additional cost for material and labor added to main cornice.

At the time the original plans were furnished by E. E. Myers, architect, his attention was called by the Superintendent to the fact that the dimension of stone to be placed in courses C and D of the main cornice was insufficient to balance itself without temporary support, until the cut stone and masonry above was placed in position, as shown by a sketch furnished by the Superintendent. Considering the risk and injury to the building which might have occurred had the work been carried out in this doubtful manner, the Board, upon the urgent recommendation of the Superintendent, decided to add sufficient material, thereby avoiding all chances of damage.

8. Changing material for floor and ceiling arches from brick to hollow-tile terra cotta level arches.

It was originally designed by the Architect to use brick for floor and ceiling arches, and upon this basis the contractors estimated the cost. Upon examination, it was deemed advisable to change the material from brick to terra cotta, and the contractors were instructed to calculate the difference in cost, which proved to be advantageous to the State, for the following reasons:

First—All wood furring and lath work would be avoided.

Second—The difference in the cost of plastering on lath work would be greater than the additional cost of substituting terra cotta for brick.

Third—All ceilings, being "straight arches" by using terra cotta, are preferable to decorators for ornamental work.

The Board, therefore, deemed it expedient to authorize the change.

PROGRESS OF THE WORK.

STATEMENT OF PROGRESS IN THE ERECTION OF THE CAPITOL BUILDING, FROM DECEMBER 1, 1890, TO NOVEMBER 30, 1892.

The cut-stone work throughout the building has been completed, standing as an everlasting monument to the resources of Colorado granite quarries. All the interior walls of brick and stone, supporting the massive trusses and the roof, are up and finished, their proportions impressing one with a sense of security.

The steel beams and girders, the brick and tile arches of the several floors of the structure are in place, ready to receive the furring and cementing preparatory to laying the floors.

A temporary flight of stairs, leading from the first floor to the third floor, has been built, for the convenience of the public and artisans.

The slate roof, skylights, copper gutters, and ventilators are practically completed. A few words with regard to the slate will not be amiss, as there are few buildings in the United States having slate equal in size, and it is doubtful if laid with more care and skill. The slates are fourteen inches wide by twenty-seven inches long, by three-eighths of an inch thick, held in place by two brass screws to each slate, the greater portion of which is bedded on cement.

The roof-drainage system has been completed, one-half of the water falling on the roof being carried into Colfax avenue and the other half into Fourteenth avenue, by means of vitrified-clay sewer pipe. The exterior window and door openings of the building have been temporarily closed, to prevent the action of the elements from damaging the floors; also for the protection of future artisan work.

The skeleton work of the dome is up to floor in bell of dome, at a height of one hundred and ninety feet and three inches above grade line of building. The contract for the remainder of the skeleton work has been let, as well as for the covering and windows of the entire dome, from roof line to top of lantern, which is to be surmounted by a statue, not yet selected.

The top of lantern will be two hundred and forty-four feet and six inches above grade line of building. The contract for covering of the dome includes the construction of a system of circular stairs and ladders, by means of which access to the floor of lantern is obtained, at a distance of two hundred and twenty-two feet above grade line of building.

From this lofty height, the grandeur of the view is beyond description. Suffice it to say, that over one hundred and fifty miles of the Rocky Mountain range, with its snowy peaks, can be seen at almost a glance, the valley and the beautiful city of Denver appearing like a huge panorama, once seen, never to be forgotten.

The main sewer system of the building has been extended to east side of Broadway.

The amount of material of various kinds used during the period of two years ending December 1, 1892, in the principal parts of the construction, is as follows:

110,882 cubic feet cut stone.
 1,700,000 brick in floor arches.
 6,817,886 brick in walls.
 101,493 cubic feet of masonry in dome walls.
 7,015 cubic feet stone backing.
 6,390 pieces of stone beam bearings.
 2,600 feet of drain pipe for roof drainage.
 370 feet main sewer system.
 493,000 pounds cast iron.
 1,234,497 pounds steel beams, etc.
 13,000 pounds of copper.
 138,000 feet B. M. lumber.
 50,700 square feet of slate.
 1,763 square feet of skylight glass.
 36,400 square feet of concrete on floor arches.

ESTIMATE OF FUNDS

REQUIRED FOR THE YEARS 1893 AND 1894, TO COMPLETE THE BUILDING.

According to the original plans of E. E. Myers, late architect, it was contemplated to finish the interior in wood, but this was at the time when the material for the construction of the building was to be sandstone. In view of the fact that granite has been used, the Board suggests that the adoption of wood for the interior finish of the building would be against all modern ideas of construction, and not at all in keeping with the edifice. So far, the building is absolutely fire-proof, but the use of combustible wood finish would not render it so; neither could it be considered durable or pleasing to the eye.

Referring to the wainscoting, the plans specify heavy paneled wood-work, which experience teaches is not desirable in this dry climate, nor reliable when used for such purposes. Changing said wood construction to marble would be more in harmony with the exterior finish of the building. Colorado marble quarries are now being rapidly developed, furnishing splendid quality of stone, and there can be no question but that the necessary quantity can be obtained here, thus further demonstrating the wonderful resources of our young State, in furnishing the splendid material for the erection of its chief public building.

The Board further desires to call your attention to the fact that the plans, as now drawn, call for the balustrades around the gallery of the House and Senate to be constructed entirely of wood. In the Board's opinion, a change to ornamental iron work would be far more safe and durable.

The plans also show the elevated floors throughout the building supported by a net work of wood construction, forming a veritable fire-trap. Changing this part of the construction to that of wrought iron, would make it fire-proof and more desirable.

As the interior finish of the doors and windows is exceedingly plain and entirely out of harmony with the exterior, a more elaborate design should be adopted in its place.

After carefully reviewing the different branches of artisan work required in the construction of the building, the Board finds that, to complete the work ready for occupancy, there will be required, as an additional appropriation, the amount of \$400,000, to be distributed among the following branches:

- Marble and tile floors.
- Marble door sills and steps.
- Marble slabs for niches.
- Marble wainscoting.
- Carpenter work.
- Hardware.
- Wrought iron work.
- Cast iron work, including grand stairs.
- Statuary for dome.
- Vault doors.
- Elevators.
- Plastering and stucco work.
- Painting and graining.
- Glazing and glass.
- Plumbing, sewer, and water connections.
- Boilers, pumps, fans, heating and ventilation.
- Fan ducts, stacks and concrete work.
- Electric plant and wiring.
- Gas fitting.
- Stair work.
- Tile partitions.
- Gallery construction in house and senate.
- Galvanized iron work.
- Balustrades around grand stairs.
- Library and dome balconies.
- Elevated floors in house and gallery of senate.
- Lamp posts and connections.
- Not including shelving, racks and counters in offices, vaults and library.

The limit of the cost of the building, after the change from sandstone to granite had been decided upon, was to be \$2,000,000. Of this amount, there has been appropriated \$1,700,000, leaving a balance of unexpended appropriation of \$300,000. Deducting therefrom amounts due contractors for unfinished work, retained percentage, and new contracts entered into but not yet commenced, estimated at \$150,000, leaves \$150,000 of the original amount appropriated unexpended.

The actual amount of cash now available, as per Secretary's report, is \$78,922.91. To this may be added as cash receipts, provided for by law through the collection of Capitol building tax for the ensuing two years, the estimated amount of \$225,000. This amount will be contingent upon the valuation of the taxable property, and the diligence with which the same will be collected.

In order to complete the work within a reasonable time, say in time for the occupancy of the building by the several departments within the next year, and for the Tenth General Assembly, if the necessary funds can be raised so that the work can be pushed as fast as possible, and to insure the prompt fulfillment of pending and future contracts, it will be necessary for the Legislature to pass such measures as will provide the Board with the necessary funds to meet every monied obligation to which they are bound.

The financial transactions of the Board are shown in the following report of the Secretary.

SECRETARY'S REPORT.

To the Board of Capitol Managers:

GENTLEMEN—I present herewith a statement of the receipts and disbursements on account of the Capitol building, for the fiscal years 1891 and 1892, showing all financial transactions from December 1st, 1890, to November 30th, 1892, inclusive.

All accounts or bills were duly allowed by the Board, and certified to the State Auditor, who drew his warrant on the State Treasurer for the amount stated on each voucher, and in favor of the owner thereof.

Respectfully,

HERMAN LUEDERS,

Secretary.

DENVER, COLO., December 1, 1892.

APPROPRIATION ACCOUNT.

<i>Dr.</i>	
To appropriations of the Fifth, Sixth and Seventh General Assemblies:	
For the year 1885.....	\$ 200,000 00
For the year 1886.....	200,000 00
For the year 1887.....	200,000 00
For the year 1888.....	200,000 00
For the year 1889.....	500,000 00
For the year 1890.....	400,000 00
For the year 1890 (grounds).....	20,000 00
Total.....	\$1,720,000 00
By disbursements:	
<i>Cr.</i>	
For the years 1885 and 1886.....	\$ 47,193 10
For the years 1887 and 1888.....	215,504 74
For the years 1889 and 1890.....	555,932 83
For the years 1891 and 1892.....	819,136 21
Balance.....	82,233 12
Total.....	\$1,720,000 00
Voucher No. 106, Rocky Mountain News Printing Company, not having been presented to Auditor before he closed his books. \$ 6 53	
Interest on bonds paid by Treasurer Carlile, for which no warrants were drawn and which the Auditor has not charged to appropriations..... 11,250 00	
	\$11,256 53
will show a balance of unexpended appropriation amounting to.....	\$93,489 65

ACCOUNT WITH TREASURER.

<i>Cr.</i>	
1892.	
Nov. 30..	By vouchers Nos. 556 to 1033, inclusive..... \$805,133 43
	By duplicate vouchers Nos. 242 and 244, not presented for payment heretofore..... 127 78
	By interest on Capitol Building bonds..... 13,875 00
	Balance..... 78,922 91
<i>Dr.</i>	
1890.	
Dec. 1..	To balance..... \$58,869 06
	To bonds—Balance first series..... \$150,000 00
	Second series..... 300,000 00
	Premium..... 5,717 00
	455,717 00
	To Internal Improvement Fund (loan)..... 150,000 00
	To Capitol Building Special Fund..... 16,000 00
	To Public Building Income Fund..... \$2,141 26
	To Public Building Permanent Fund... 4,220 21
	6,361 47
	To taxes collected, 1891..... \$102,779 82
	To taxes collected, 1892..... 108,331 77
	211,111 59
	\$898,059 12
	\$898,059 12
Balance, as per Secretary's report..... \$78,922 91	
Balance, as per Treasurer's report..... \$79,636 28	
Less vouchers not presented when Treasurer closed his books:	
	Voucher No. 886, M. Chiuilli..... \$11 00
	Voucher No. 1016, Rocky Mountain News..... 6 53
	Voucher No. 1022, J. Fitzgerald..... 487 50
	Voucher No. 1028, Otto Mears..... 208 34
	713 37
Balance to credit of Capitol Building Fund..... \$78,922 91	
	\$78,922 91

CAPITOL BUILDING "SPECIAL FUND ACCOUNT."

The receipts on this account are the proceeds from the sale of lots donated by citizens of Denver for aiding in the erection of the State Capitol building, at Denver, Colorado; now sold.

<i>Dr.</i>	
To balance.....	\$16,000 00
To cash received, balance of payment for lots 1 to 24, inclusive, block 81, Brown, Smith & Porter's addition.....	16,000 00
	\$32,000 00
<i>Cr.</i>	
By vouchers drawn on this fund for actual construction of building:	
No. 699, Geddis & Seerie.....	\$30,269 85
No. 898, Lane Bridge and Iron Works.....	1,730 15
	\$32,000 00

CAPITOL BUILDING GROUNDS ACCOUNT.

<i>Dr.</i>		
To balance.....		\$17,252 00
By vouchers drawn: <i>Cr.</i>		
Nos. 654, 691, 703, 882, 902, 938, 943, 944, 945, 946, 966, 1010, 1020,	\$2,604 86	
Balance.....	14,647 14	\$17,252 00

W. D. RICHARDSON LABOR RELIEF ACCOUNT.

<i>Dr.</i>		
To appropriation.....		\$5,000 00
By 93 vouchers drawn: <i>Cr.</i>		
Nos. 738-804, 812-818, 829-830, 848-849, 865-867, 886-887, 903-905, 922, 963-965, 981, 1022-1023, inclusive	\$4,185 77	
Balance.....	814 23	\$5,000 00

RETAINED PAYMENTS ACCOUNT.

Geddis & Seerie.....	\$35,917 08
Lane Bridge and Iron Works, Contract 1.....	1,013 50
Lane Bridge and Iron Works, Contract 2.....	1,728 99
W. J. Godfrey & Co.....	440 89
The Colorado Iron Works.....	810 19
Fred. Stapp.....	1,574 22
	\$41,484 87

SUMMARY OF DISBURSEMENT ACCOUNTS, 1891 AND 1892.

General building account	\$756,743 70
Salaries	15,999 98
Managers' salaries.....	19,406 78
Expenses—	
Office of Secretary.....	308 18
Office of Superintendent.....	3,169 11
Printing and advertising.....	759 06
Legal account.....	1,000 00
Miscellaneous account.....	64 50
Bond account.....	1,019 27
Capitol building grounds	2,604 86
W. D. Richardson labor relief.....	4,185 77
Interest.....	13,875 00
	\$819,136 21

LIST OF VOUCHERS.

DATE.	NO.	TO WHOM PAID.	WHAT FOR.	AMOUNT.
1890.				
Dec. 3..	556	Geddis & Seerie.....	29th Est., superstructure	\$31,394 22
Dec. 3..	557	Colo. Iron Works, assignees of W. J. Godfrey & Co.....	7th estimate, iron columns..	927 94
Dec. 3..	558	Geddis & Seerie	Grouting walls.....	328 71
Dec. 3..	559	R. W. Stewart & Co.....	Lumber.....	23 60
Dec. 3..	560	Lane Bridge and Iron Works.	12th estimate, steel beams..	382 34
Dec. 3..	561	McPhee & McGinnity.....	Lumber	326 69
Dec. 3..	562	C. J. Reilly.....	Soil pipe.....	495 80
Dec. 3..	563	Stone & Locke Book and Stationery Company.....	Repairing frames.....	14 00
Dec. 31..	564	John L. Routt	Manager's compensation...	208 33
Dec. 31..	565	Otto Mears.....	Manager's compensation...	208 33
Dec. 31..	566	Benj. F. Crowell.....	Manager's compensation...	208 33
Dec. 31..	567	Chas. J. Hughes, Jr.....	Manager's compensation...	208 33
Dec. 31..	568	Peter Gumry.....	Salary as Superintendent...	300 00
Dec. 31..	569	Thomas Mullen.....	Salary as Asst. Supt.....	200 00
Dec. 31..	570	Herman Lueders.....	Salary as Secretary.....	166 65
1891.				
Jan. 7..	571	Geddis & Seerie.....	30th Est., superstructure	41,187 11
Jan. 7..	572	Geddis & Seerie.....	Change of windows in east portico; grouting walls..	682 50
Jan. 7..	573	Colo. Iron Works, assignees of W. J. Godfrey & Co.....	8th Est., iron columns.....	1,763 10
Jan. 7..	574	McPhee & McGinnity.....	Lumber	311 78
Jan. 7..	575	C. J. Reilly.....	Soil pipe.....	499 15
Jan. 7..	576	Colorado Telephone Co.....	Office expenses, Secretary..	20 00
Jan. 7..	577	Peter Gumry.....	Office expenses, Supt.....	12 40
Jan. 7..	578	Helen S. Woods.....	Copying reports.....	16 00
Jan. 7..	579	S. P. Spencer.....	Cert. copy lease of quarry..	3 00
Jan. 7..	580	Herman Lueders	Office expenses, Secretary ..	4 25
Jan. 31..	581	John L. Routt	Manager's compensation...	87 36
Jan. 31..	582	Otto Mears.....	Manager's compensation...	208 33
Jan. 31..	583	Benj. F. Crowell.....	Manager's compensation...	208 33
Jan. 31..	584	Chas. J. Hughes, Jr.....	Manager's compensation...	208 33
Jan. 31..	585	Peter Gumry.....	Salary as Superintendent...	300 00
Jan. 31..	586	Thomas Mullen.....	Salary as Asst. Supt.....	200 00
Jan. 31..	587	Herman Lueders.....	Salary as Secretary.....	166 66

LIST OF VOUCHERS—Continued.

DATE.	NO.	TO WHOM PAID.	WHAT FOR.	AMOUNT.
1891.				
Feb. 4..	588	Geddis & Seerie.....	31st Est., superstructure....	\$15,649 68
Feb. 4..	589	Lane Bridge and Iron Works.	13th Est., setting beams.....	788 83
Feb. 4..	590	Colo. Iron Works, assignees of W. J. Godfrey & Co.....	9th estimate, iron columns..	761 40
Feb. 4..	591	Colorado Iron Works.....	Two extra columns.....	175 00
Feb. 4..	592	C. J. Reilly.....	Soil pipe.....	129 00
Feb. 4..	593	Jones & Riddell.....	Legal services.....	500 00
Feb. 4..	594	Harry Tarbell.....	Bonds.....	25 00
Feb. 28..	595	Otto Mears.....	Manager's compensation...	208 34
Feb. 28..	596	Benj. F. Crowell.....	Manager's compensation...	208 34
Feb. 28..	597	Chas. J. Hughes, Jr.....	Manager's compensation...	208 34
Feb. 28..	598	Peter Gumry.....	Salary as Superintendent...	300 00
Feb. 28..	599	Thomas Mullen.....	Salary as Asst. Supt.....	200 00
Feb. 28..	600	Herman Lueders.....	Salary as Secretary.....	166 68
Mar. 4..	601	Geddis & Seerie.....	32d Est., superstructure....	18,111 10
Mar. 4..	602	Colo. Iron Works, assignees of W. J. Godfrey & Co.....	10th estimate, iron columns..	1,450 73
Mar. 4..	603	Herman Lueders.....	Office expenses, Secretary..	6 25
Mar. 4..	604	Gazette Printing Company..	1,000 reports.....	200 00
Mar. 31..	605	Otto Mears.....	Manager's compensation...	208 33
Mar. 31..	606	Benj. F. Crowell.....	Manager's compensation...	208 33
Mar. 31..	607	Chas. J. Hughes, Jr.....	Manager's compensation...	208 33
Mar. 31..	608	Peter Gumry.....	Salary as Superintendent...	300 00
Mar. 31..	609	Thomas Mullen.....	Salary as Asst. Supt.....	200 00
Mar. 31..	610	Herman Lueders.....	Salary as Secretary.....	166 66
April 1..	611	Geddis & Seerie.....	33d Est., superstructure....	21,078 11
April 1..	612	Geddis & Seerie.....	Grouting walls.....	288 69
April 1..	613	Denver Omnibus and Car- riage Company.....	Conveyances, Gen. Assembly	34 00
April 30..	614	Otto Mears.....	Manager's compensation...	208 33
April 30..	615	Benj. F. Crowell.....	Manager's compensation...	208 33
April 30..	616	Chas. J. Hughes, Jr.....	Manager's compensation...	208 33
April 30..	617	Job A. Cooper.....	Manager's compensation...	152 75
April 30..	618	Peter Gumry.....	Salary as Superintendent...	300 00
April 30..	619	Thomas Mullen.....	Salary as Asst. Supt.....	200 00

LIST OF VOUCHERS—Continued.

DATE.	NO.	TO WHOM PAID.	WHAT FOR.	AMOUNT.
1891.				
April 30..	620	Herman Lueders.....	Salary as Secretary.....	\$166 65
May 6..	621	Geddis & Seerie.....	34th Est., superstructure....	36,537 91
May 6..	622	Geddis & Seerie.....	Grouting walls.....	615 33
May 6..	623	Colo. Iron Works, assignees of W. J. Godfrey & Co.....	11th Est., iron columns.....	900 00
May 6..	624	McPhee & McGinnity.....	Lumber.....	23 90
May 6..	625	Peter Gumry.....	Cash advanced; services of assistant.....	138 00
May 6..	626	Colorado Telephone Co.....	Office expenses, Secretary..	20 00
May 6..	627	Herman Lueders.....	Office expenses, Secretary..	5 00
May 30..	628	Otto Mears.....	Manager's compensation...	208 34
May 30..	629	Benj. F. Crowell.....	Manager's compensation...	208 34
May 30..	630	Chas. J. Hughes, Jr.....	Manager's compensation...	208 34
May 30..	631	Job A. Cooper.....	Manager's compensation...	208 34
May 30..	632	Peter Gumry.....	Salary as Superintendent...	300 00
May 30..	633	Thomas Mullen.....	Salary as Asst. Supt.....	200 00
May 30..	634	Herman Lueders.....	Salary as Secretary.....	166 69
June 4..	635	Geddis & Seerie.....	35th Est., superstructure....	30,319 77
June 4..	636	Geddis & Seerie.....	Fluting pilaster caps and grouting walls.....	2,015 63
June 4..	637	Peter Gumry.....	Cash adv., services of asst..	271 26
June 4..	638	McPhee & McGinnity.....	Lumber.....	48 70
June 4..	639	C. J. Kelly.....	Printing.....	46 25
June 4..	640	W. H. Lawrence & Co.....	One cabinet.....	22 50
June 4..	641	Abstract Title and Ins. Co...	Abstract.....	12 50
June 4..	642	Lane Bridge and Iron Works	14th Est., retained per cent.	1,421 50
June 30..	643	Otto Mears.....	Manager's compensation...	208 33
June 30..	644	Benj. F. Crowell.....	Manager's compensation...	208 33
June 30..	645	Chas. J. Hughes, Jr.....	Manager's compensation...	208 33
June 30..	646	Job A. Cooper.....	Manager's compensation...	208 33
June 30..	647	Peter Gumry.....	Salary as Superintendent..	300 00
June 30..	648	Thomas Mullen.....	Salary as Asst. Supt.....	200 00
June 30..	649	Herman Leuders.....	Salary as Secretary.....	166 66
July 1..	650	Geddis & Seerie.....	36th Est., superstructure....	32,812 59
July 1..	651	Geddis & Seerie.....	Setting pipe, smoke-stack, and grouting walls.....	1,285 64

LIST OF VOUCHERS—Continued.

DATE.	NO.	TO WHOM PAID.	WHAT FOR.	AMOUNT.
1891.				
July 1..	652	Lane Bridge and Iron Works.	15th Est., erecting beams, 3d floor.....	\$560 49
July 1..	653	Peter Gumry.....	Cash advanced; services of assistant, etc.....	153 00
July 1..	654	Peter Gumry.....	Material and labor, repairing sidewalk on Broadway	34 96
July 1..	655	Colorado Telephone Co.....	Office expenses, Secretary..	20 00
July 1..	656	Engineering News Pub. Co..	Advertising proposals.....	18 80
July 1..	657	Engineering Record.....	Advertising proposals.....	22 00
July 1..	658	Denver Times Pub. Co.....	Advertising proposals.....	52 50
July 1..	659	Republican Publishing Co..	Advertising proposals.....	56 40
July 1..	660	Rocky Mountain News Printing Company.....	Advertising proposals.....	56 40
July 1..	661	Colorado Sun.....	Advertising proposals.....	47 85
July 31..	662	Otto Mears.....	Manager's compensation...	208 33
July 31..	663	Benj. F. Crowell.....	Manager's compensation...	208 33
July 31..	664	Chas. J. Hughes, Jr.....	Manager's compensation...	208 33
July 31..	665	Job A. Cooper.....	Manager's compensation...	208 33
July 31..	666	Peter Gumry.....	Salary as Superintendent...	300 00
July 31..	667	Thomas Mullen.....	Salary as Asst. Supt.....	200 00
July 31..	668	Herman Lueders.....	Salary as Secretary.....	166 67
Aug. 5..	669	Geddis & Seerie.....	37th Est., superstructure...	44,266 41
Aug. 5..	670	Geddis & Seerie.....	Grouting walls.....	262 50
Aug. 5..	671	Colo. Iron Works, assignees of W. J. Godfrey & Co....	12th estimate, iron columns	399 60
Aug. 5..	672	Lane Bridge and Iron Works.	1st Est., 2nd contract, steel beams.....	180 31
Aug. 5..	673	Lane Bridge and Iron Works.	14 Z-bar columns under galleries.....	300 00
Aug. 5..	674	Colorado Iron Works.....	Smoke stack.....	56 10
Aug. 5..	675	McPhee & McGinnity.....	Lumber.....	9 55
Aug. 5..	676	C. J. Reilly.....	Pipe.....	10 00
Aug. 5..	677	Peter Gumry.....	Cash advanced; services of assistant.....	152 25
Aug. 5..	678	Katherine Grace.....	Type writing.....	6 00
Aug. 5..	679	Herman Lueders.....	Office expenses, Secretary..	7 00
Aug. 31..	680	Otto Mears.....	Manager's compensation...	208 34
Aug. 31..	681	Benj. F. Crowell.....	Manager's compensation...	208 34

LIST OF VOUCHERS—Continued.

DATE.	NO.	TO WHOM PAID.	WHAT FOR.	AMOUNT.
1891.				
Aug. 31..	682	Chas. J. Hughes, Jr.....	Manager's compensation...	\$208 34
Aug. 31..	683	Job A. Cooper.....	Manager's compensation...	208 34
Aug. 31..	684	Peter Gumry.....	Salary as Superintendent..	300 00
Aug. 31..	685	Thomas Mullen.....	Salary as Asst. Supt.....	200 00
Aug. 31..	686	Herman Lueders.....	Salary as Secretary.....	166 67
Sept. 2..	687	Geddis & Seerie.....	38th Est., superstructure...	35,429 72
Sept. 2..	688	Geddis & Seerie.....	Grouting walls.....	75 00
Sept. 2..	689	Lane Bridge and Iron Works.	2d Est., 2d contract, steel beams.....	3,566 96
Sept. 2..	690	Peter Gumry.....	Cash advanced; services of assistant.....	155 95
Sept. 2..	691	James F. Adams, Treasurer.	License; sewer tax.....	70 25
Sept. 30..	692	Otto Mears.....	Manager's compensation...	208 33
Sept. 30..	693	Benj. F. Crowell.....	Manager's compensation...	208 33
Sept. 30..	694	Chas. J. Hughes, Jr.....	Manager's compensation...	208 33
Sept. 30..	695	Job A. Cooper.....	Manager's compensation...	208 33
Sept. 30..	696	Peter Gumry.....	Salary as Superintendent..	300 00
Sept. 30..	697	Thomas Mullen.....	Salary as Asst. Supt.....	200 00
Sept. 30..	698	Herman Lueders.....	Salary as Secretary.....	166 67
Oct. 7..	699	Geddis & Seerie.....	39th Est., superstructure...	30,269 85
Oct. 7..	700	Geddis & Seerie.....	Grouting walls.....	150 00
Oct. 7..	701	Lane Bridge and Iron Works.	3d Est., 2d contract, steel beams and channels.....	4,180 06
Oct. 7..	702	Colorado Iron Works.....	Four pieces of stack.....	158 70
Oct. 7..	703	Peter Gumry.....	Cash advanced; material and labor on water closets.	397 15
Oct. 7..	704	Collier & Cleaveland Lith. Co	Letter heads and envelopes.	16 50
Oct. 7..	705	Colorado Telephone Co.....	Office expenses, Secretary..	20 00
Oct. 7..	706	Peter Gumry.....	Cash advanced; services of assistant.....	156 00
Oct. 31..	707	Job A. Cooper.....	Manager's compensation...	208 33
Oct. 31..	708	Otto Mears.....	Manager's compensation...	208 33
Oct. 31..	709	Benj. F. Crowell.....	Manager's compensation...	208 33
Oct. 31..	710	Chas. J. Hughes, Jr.....	Manager's compensation...	208 33
Oct. 31..	711	Peter Gumry.....	Salary as Superintendent..	300 00
Oct. 31..	712	Thomas Mullen.....	Salary as Asst. Supt.....	200 00

LIST OF VOUCHERS—Continued.

DATE.	NO.	TO WHOM PAID.	WHAT FOR.	AMOUNT.
1891.				
Oct. 31..	713	Herman Lueders.....	Salary as Secretary.....	\$166 66
Nov. 4..	714	Geddis & Seerie.....	40th Est., superstructure ..	27,778 33
Nov. 4..	715	Geddis & Seerie.....	Carving caps of columns; grouting walls.....	2,950 00
Nov. 4..	716	Lane Bridge and Iron Works.	4th Est., 2d contract, beams and girders.....	7,241 63
Nov. 4..	717	Peter Gumry.....	Cash advanced; services of assistant, etc.....	178 30
Nov. 4..	718	Rocky Mt. News Ptg. Co....	Advertising.....	7 70
Nov. 4..	719	Republican Publishing Co..	Advertising.....	8 25
Nov. 4..	720	The Colorado Sun.....	Advertising.....	4 35
Nov. 4..	721	Denver Times Pub Co.....	Advertising.....	4 35
Nov. 4..	722	C J. Kelly.....	Printing.....	4 25
Nov. 4..	723	Herman Lueders.....	Office expenses, Secretary ..	11 15
Nov. 30..	724	Job A. Cooper.....	Manager's compensation... ..	208 34
Nov. 30..	725	Otto Mears.....	Manager's compensation... ..	208 34
Nov. 30..	726	Benj. F. Crowell.....	Manager's compensation... ..	208 34
Nov. 30..	727	Chas. J. Hughes, Jr.....	Manager's compensation... ..	208 34
Nov. 30..	728	Peter Gumry.....	Salary as Superintendent... ..	300 00
Nov. 30..	729	Thomas Mullen.....	Salary as Asst. Supt.....	200 00
Nov. 30..	730	Herman Lueders.....	Salary as Secretary.....	166 67
Dec. 2..	731	Geddis & Seerie.....	41st Est., superstructure... ..	33,693 36
Dec. 2..	732	Geddis & Seerie.....	Grouting walls.....	120 00
Dec. 2..	733	Lane Bridge and Iron Works.	5th Est., 2d contract, beams and channels.....	3,591 28
Dec. 2..	734	Colorado Iron Works.....	Tie-rods and labor.....	25 89
Dec. 3..	735	Fred. Stapp.....	1st Est., asbestos paper and screws.....	1,953 80
Dec. 3..	736	Peter Gumry.....	Cash advanced; services of assistant.....	144 00
Dec. 10..	737	C. H. McLaughlin.....	Expenses; error in deed....	15 00
Dec. 16..	738	James Neville.....	Unpaid labor under Richardson	24 00
Dec. 16..	739	Thomas Casey.....	" " "	11 00
Dec. 16..	740	Byron A. Neville.....	" " "	29 37
Dec. 16..	741	John Caton.....	" " "	22 00
Dec. 16..	742	H. H. Bragg.....	" " "	14 00
Dec. 16..	743	John H. Routt.....	" " "	387 50

LIST OF VOUCHERS—Continued.

DATE.	NO.	TO WHOM PAID.	WHAT FOR.	AMOUNT.
1891.				
Dec. 16..	744	Louis Graff.....	Unpaid labor under Richardson	\$4 00
Dec. 16..	745	Chas. F. Lindblad.....	" " "	22 00
Dec. 16..	746	Charles Peterson.....	" " "	22 00
Dec. 16..	747	James M. Stoner.....	" " "	11 00
Dec. 16..	748	George Brantigam.....	" " "	11 00
Dec. 16..	749	Charles Aurr.....	" " "	11 00
Dec. 16..	750	Simon Rottner.....	" " "	11 00
Dec. 16..	751	John W. Dashem.....	" " "	11 00
Dec. 16..	752	H. C. Neville.....	" " "	41 87
Dec. 16..	753	Michael Labriola.....	" " "	22 00
Dec. 16..	754	Thomas McIntyre.....	" " "	11 00
Dec. 16..	755	J. C. Seavey.....	" " "	11 00
Dec. 16..	756	Charles A. Lindwall.....	" " "	52 00
Dec. 16..	757	Cæsar Tettamanti.....	" " "	22 00
Dec. 16..	758	George H. Buckingham.....	" " "	31 50
Dec. 16..	759	Antonio Tolosi.....	" " "	22 00
Dec. 16..	760	Phillip Reitz.....	" " "	12 80
Dec. 16..	761	C. S. Abbott.....	" " "	100 00
Dec. 16..	762	John A. Borjenson.....	" " "	31 87
Dec. 16..	763	C. Emil Johnson.....	" " "	11 00
Dec. 16..	764	Frank Bildner.....	" " "	73 00
Dec. 16..	765	Charles Vetter.....	" " "	75 00
Dec. 16..	766	E. F. Vincent.....	" " "	329 17
Dec. 16..	767	James Nicholson.....	" " "	9 75
Dec. 16..	768	James Gilmore.....	" " "	22 00
Dec. 16..	769	P. J. O'Neill.....	" " "	11 00
Dec. 16..	770	Frank Berger.....	" " "	15 00
Dec. 16..	771	Lawrence Conway.....	" " "	11 00
Dec. 16..	772	Timothy Ryan.....	" " "	42 50
Dec. 16..	773	Thomas Goodson.....	" " "	11 00
Dec. 16..	774	Charles Downham.....	" " "	11 00
Dec. 16..	775	John L. Vandeman.....	" " "	13 50
Dec. 16..	776	Patrick Walsh.....	" " "	11 00
Dec. 16..	777	Michael Rossi.....	" " "	11 00

LIST OF VOUCHERS—Continued.

DATE.	NO.	TO WHOM PAID.	WHAT FOR.	AMOUNT.
1891.				
Dec. 16..	778	Frank A. Honecker.....	Unpaid labor under Richardson	\$300 00
Dec. 16..	779	Joseph Roy.....	" " "	14 00
Dec. 16..	780	Anthony Burke.....	" " "	5 00
Dec. 16..	781	Frederick L. Des Moineaux.	" " "	46 85
Dec. 16..	782	John Pomeroy.....	" " "	46 85
Dec. 16..	783	Peter Melquist.....	" " "	11 00
Dec. 16..	784	John Riordan.....	" " "	11 00
Dec. 16..	785	Marco Rosi.....	" " "	11 00
Dec. 16..	786	Mary L. De Lange.....	" " "	82 00
Dec. 16..	787	Bernhard Peterson.....	" " "	11 00
Dec. 16..	788	Richard Pomeroy.....	" " "	31 87
Dec. 16..	789	Daniel Shea.....	" " "	39 37
Dec. 16..	790	John Berggren.....	" " "	11 00
Dec. 16..	791	Vito Loviso.....	" " "	11 00
Dec. 16..	792	Arthur Carlson.....	" " "	11 00
Dec. 16..	793	Ody Sheldon.....	" " "	11 00
Dec. 16..	794	Nicholas Steinmetz.....	" " "	22 00
Dec. 16..	795	M. J. McGrath.....	" " "	12 50
Dec. 16..	796	Philip Horn.....	" " "	22 00
Dec. 16..	797	Frank Dondero.....	" " "	22 50
Dec. 16..	798	George Ferguson.....	" " "	11 00
Dec. 16..	799	Andrew Lindquist.....	" " "	11 00
Dec. 16..	800	Mark Jeffry.....	" " "	11 00
Dec. 16..	801	L. J. Wheeler.....	" " "	100 00
Dec. 16..	802	George Isaacs.....	" " "	11 00
Dec. 16..	803	T. E. Gray.....	" " "	39 00
Dec. 16..	804	Charles A. Chadwick.....	" " "	23 00
Dec. 31..	805	Job A. Cooper.....	Manager's compensation...	208 33
Dec. 31..	806	Otto Mears.....	Manager's compensation...	208 33
Dec. 31..	807	Benj. F. Crowell.....	Manager's compensation...	208 33
Dec. 31..	808	Chas. J. Hughes, Jr.....	Manager's compensation...	208 33
Dec. 31..	809	Peter Gumry.....	Salary as Superintendent...	300 00
Dec. 31..	810	Thomas Mullen.....	Salary as Asst. Supt.....	200 00
Dec. 31..	811	Herman Lueders.....	Salary as Secretary.....	166 66

LIST OF VOUCHERS—Continued.

DATE.	NO.	TO WHOM PAID.	WHAT FOR.	AMOUNT.
1892.				
Jan. 6..	812	John Luebbers.....	Unpaid labor under Richardson	\$11 00
Jan. 6..	813	John B. Morris.....	" " "	75 00
Jan. 6..	814	L. Colombos.....	" " "	11 00
Jan. 6..	815	Frank John.....	" " "	11 00
Jan. 6..	816	Mike Barra.....	" " "	22 00
Jan. 6..	817	Bernhard Scheuring.....	" " "	75 00
Jan. 6..	818	James Biggers.....	" " "	8 00
Jan. 6..	819	W. B. Dana & Co.....	Advertising.....	10 00
Jan. 6..	820	Denver Times Pub. Co.....	Advertising.....	11 75
Jan. 6..	821	The Colorado Sun.....	Advertising.....	12 70
Jan. 6..	822	Republican Pub. Co.....	Advertising.....	21 00
Jan. 6..	823	Rocky Mt. News Ptg. Co.....	Advertising.....	20 80
Jan. 6..	824	Colorado Telephone Co.....	Office expenses, Secretary ..	20 00
Jan. 6..	825	Peter Gumry.....	Cash advanced; services of assistant, etc.....	173 15
Jan. 6..	826	Geddis & Seerie.....	Addition to main cornice, and grouting walls.....	4,864 95
Jan. 6..	827	Geddis & Seerie.....	42d Est., superstructure ...	32,482 60
Jan. 6..	828	Lane Bridge and Iron Works.	6th Est., 2d contract, beams and channels.....	9,723 76
Jan. 18..	829	S. A. Carlson.....	Unpaid labor under W. D. Richardson.....	75 00
Jan. 18..	830	Olof Bergstrom.....	Unpaid labor under W. D. Richardson.....	11 00
Jan. 31..	831	Job A. Cooper.....	Manager's compensation...	208 33
Jan. 31..	832	Otto Mears.....	Manager's compensation...	208 33
Jan. 31..	833	Benj. F. Crowell.....	Manager's compensation...	208 33
Jan. 31..	834	Chas. J. Hughes, Jr.....	Manager's compensation...	208 33
Jan. 31..	835	Peter Gumry.....	Salary as Superintendent ..	300 00
Jan. 31..	836	Thomas Mullen.....	Salary as Asst. Supt.....	200 00
Jan. 31..	837	Herman Lueders.....	Salary as Secretary.....	166 67
Feb. 3..	838	Frank Anderson.....	1st Est., roof sheeting	2,232 00
Feb. 3..	839	Geddis & Seerie.....	43d Est., superstructure ...	16,450 78
Feb. 3..	840	Geddis & Seerie.....	Carving caps of columns and grouting walls.....	4,137 50
Feb. 3..	841	Lane Bridge and Iron Works.	7th Est., 2d contract, beams, channels, etc.....	8,509 37

LIST OF VOUCHERS — *Continued.*

DATE.	NO.	TO WHOM PAID.	WHAT FOR.	AMOUNT.
1892.				
Feb. 3..	842	Colorado Iron Works.....	Tie rod and labor.....	\$37 53
Feb. 3..	843	Peter Gumry.....	Cash advanced; services of assistant, etc.....	166 10
Feb. 3..	844	Lester G. Brewer.....	Cash advanced; telegrams..	13 95
Feb. 3..	845	The Sun Publishing Co.....	Advertising.....	14 30
Feb. 3..	846	Republican Publishing Co...	Advertising.....	13 05
Feb. 3..	847	Herman Lueders.....	Office expenses, Secretary..	6 25
Feb. 3..	848	John Reynolds.....	Unpaid labor under W. D. Richardson.....	11 00
Feb. 3..	849	Frank Whittaker.....	Unpaid labor under W. D. Richardson.....	24 00
Feb. 29..	850	Job A. Cooper.....	Manager's compensation...	208 34
Feb. 29..	851	Otto Mears.....	Manager's compensation...	208 34
Feb. 29..	852	Benj. F. Crowell.....	Manager's compensation...	208 34
Feb. 29..	853	Chas. J. Hughes, Jr.....	Manager's compensation...	208 34
Feb. 29..	854	Peter Gumry.....	Salary as Superintendent..	300 00
Feb. 29..	855	Thomas Mullen.....	Salary as Asst. Supt.....	200 00
Feb. 29..	856	Herman Lueders.....	Salary as Secretary.....	166 67
Mar. 4..	857	Geddis & Seerie.....	44th Est., superstructure...	20,362 46
Mar. 4..	858	Lane Bridge and Iron Works.	8th Est., 2d contract, beams, channels, etc.....	13,571 25
Mar. 4..	859	Fred. Stapp.....	2d estimate, slate.....	479 59
Mar. 4..	860	Geddis & Seerie.....	Addition to main cornice; grouting walls.....	5,756 90
Mar. 4..	861	Colorado Iron Works.....	Tie rod and labor.....	29 63
Mar. 4..	862	Peter Gumry.....	Cash advanced; services of assistant.....	114 00
Mar. 4..	863	C. J. Kelly.....	Printing vouchers.....	12 50
Mar. 4..	864	Rocky Mt. News Ptg. Co.....	Advertising.....	14 30
Mar. 4..	865	Charles H. Garland.....	Unpaid labor under W. D. Richardson.....	72 00
Mar. 4..	866	Charles Boettcher.....	Unpaid labor under W. D. Richardson.....	600 00
Mar. 4..	867	John Miller.....	Unpaid labor under W. D. Richardson.....	17 00
Mar. 31..	868	Job A. Cooper.....	Manager's compensation...	208 33
Mar. 31..	869	Otto Mears.....	Manager's compensation...	208 33
Mar. 31..	870	Benj. F. Crowell.....	Manager's compensation...	208 33

LIST OF VOUCHERS — *Continued.*

DATE.	NO.	TO WHOM PAID.	WHAT FOR.	AMOUNT.
1892.				
Mar. 31..	871	Chas. J. Hughes, Jr.....	Manager's compensation...	\$208 33
Mar. 31..	872	Peter Gumry.....	Salary as Superintendent..	300 00
Mar. 31..	873	Thomas Mullen.....	Salary as Asst. Supt.....	200 00
Mar. 31..	874	Herman Lueders.....	Salary as Secretary.....	166 66
April 6..	875	Geddis & Seerie.....	45th Est., superstructure...	21,391 13
April 6..	876	Lane Bridge and Iron Works.	9th Est., 2d contract, beams, channels and columns...	6,054 43
April 6..	877	Fred. Stapp.....	3d estimate, slate.....	1,440 97
April 6..	878	Frank Anderson.....	2d Est., roof sheeting.....	581 04
April 6..	879	Geddis & Seerie.....	1st Est., roof drainage.....	900 00
April 6..	880	Geddis & Seerie.....	Grouting walls.....	175 00
April 6..	881	Colorado Iron Works.....	Tie rod and labor.....	31 14
April 6..	882	Small Bros.....	Repairs on closets.....	13 60
April 6..	883	Peter Gumry.....	Cash advanced; services of assistant, etc.....	162 75
April 6..	884	Colorado Telephone Co.....	Office expenses, Secretary..	20 00
April 6..	885	Herman Lueders.....	Office expenses, Secretary..	5 00
April 6..	886	Marianni Chiulli.....	Unpaid labor under W. D. Richardson.....	11 00
April 6..	887	Pierce E. Roberts.....	Unpaid labor under W. D. Richardson.....	3 00
April 16..	888	Geddis & Seerie.....	46th Est., retained per cent.	50,000 00
April 30..	889	Job A. Cooper.....	Manager's compensation...	208 33
April 30..	890	Otto Mears.....	Manager's compensation...	208 33
April 30..	891	Benj. F. Crowell.....	Manager's compensation...	208 33
April 30..	892	Chas. J. Hughes, Jr.....	Manager's compensation...	208 33
April 30..	893	Peter Gumry.....	Salary as Superintendent..	300 00
April 30..	894	Thomas Mullen.....	Salary as Asst. Supt.....	200 00
April 30..	895	Herman Lueders.....	Salary as Secretary.....	166 67
May 4..	896	Geddis & Seerie.....	47th Est., superstructure...	5,977 48
May 4..	897	Geddis & Seerie.....	2d Est., roof drainage.....	810 00
May 4..	898	Lane Bridge and Iron Works.	10th Est., 2d contract, beams, girders and columns....	4,039 39
May 4..	899	Geddis & Seerie.....	Altering west front steps...	972 50
May 4..	900	Peter Gumry.....	Cash advanced; services of assistant.....	156 00
May 4..	901	H. B. Babb.....	Legal services.....	500 00

LIST OF VOUCHERS—Continued.

DATE.	NO.	TO WHOM PAID.	WHAT FOR.	AMOUNT.
1892. May 4..	902	Geo. H. Angell.....	Surveying and establishing grades of grounds.....	\$200 00
May 4..	903	Simon Morgenthaler.....	Unpaid labor under W. D. Richardson.....	16 00
May 4..	904	John C. Luvey.....	Unpaid labor under W. D. Richardson.....	22 00
May 4..	905	Nick Kopp.....	Unpaid labor under W. D. Richardson.....	12 00
May 4..	906	Lane Bridge and Iron Works.	11th Est., 2d contract, retained per centage.....	4,000 00
May 31..	907	Job A. Cooper.....	Manager's compensation...	208 34
May 31..	908	Otto Mears.....	Manager's compensation...	208 34
May 31..	909	Benj. F. Crowell.....	Manager's compensation...	208 34
May 31..	910	Chas. J. Hughes, Jr.....	Manager's compensation...	208 34
May 31..	911	Peter Gumry.....	Salary as Superintendent...	300 00
May 31..	912	Thomas Mullen.....	Salary as Asst. Supt.....	200 00
May 31..	913	Herman Lueders.....	Salary as Secretary.....	166 67
June 1..	914	Geddis & Seerie.....	48th Est., superstructure...	2,610 60
June 1..	915	Lane Bridge and Iron Works	12th Est., 2d contract, beams, columns, etc.....	5,229 50
June 1..	916	Fred. Stapp.....	4th estimate, slate.....	1,052 89
June 1..	917	Geddis & Seerie.....	3d estimate, roof drainage..	290 00
June 1..	918	Peter Gumry.....	Cash advanced; services of assistant, etc.....	177 30
June 1..	919	New York Bank Note Co....	Eng. and printing bonds....	700 00
June 1..	920	Denver Times Pub. Co....	Advertising.....	13 05
June 1..	921	Katharine Grace.....	Typewriting—Secretary....	2 45
June 1..	922	John Davis.....	Unpaid labor under W. D. Richardson.....	7 50
June 30..	923	Job A. Cooper.....	Manager's compensation...	208 33
June 30..	924	Otto Mears.....	Manager's compensation...	208 33
June 30..	925	Benj. F. Crowell.....	Manager's compensation...	208 33
June 30..	926	Chas. J. Hughes, Jr.....	Manager's compensation...	208 33
June 30..	927	Peter Gumry.....	Salary as Superintendent...	300 00
June 30..	928	Thomas Mullen.....	Salary as Asst. Supt.....	200 00
June 30..	929	Herman Lueders.....	Salary as Secretary.....	166 66
July 6..	930	Geddis & Seerie.....	49th Est., superstructure....	4,398 48
July 6..	931	Lane Bridge and Iron Works.	13th Est., 2d contract, beams, channels and columns...	2,341 21

LIST OF VOUCHERS—Continued.

DATE.	NO.	TO WHOM PAID.	WHAT FOR.	AMOUNT.
1892. July 6..	932	Fred. Stapp.....	5th Est., slate and copper..	\$3,631 28
July 6..	933	Lane Bridge and Iron Works.	Material and labor.....	62 02
July 6..	934	Colorado Iron Works.....	Material and labor.....	26 05
July 6..	935	R. W. Stewart & Co.....	Lumber.....	10 35
July 6..	936	Peter Gumry.....	Cash advanced; services of assistant.....	160 25
July 6..	937	John M. Henderson.....	Traveling expenses to New York and return.....	200 62
July 6..	938	George H. Angell.....	Services as Superintendent grading grounds.....	300 00
July 6..	939	Colorado Telephone Co.....	Office expenses, Secretary..	20 00
July 6..	940	Herman Lueders.....	Office expenses, Secretary..	7 00
July 6..	941	Hughes & Keith S. S. Co....	Office expenses, Secretary..	2 50
July 6..	942	Geddis & Seerie.....	Carving caps of columns; changing facing to steps..	2,822 12
July 6..	943	Thomas J. Scanlon.....	Grading Capitol grounds...	1,143 00
July 6..	944	Rocky Mt. News Ptg. Co....	Advertising.....	8 70
July 6..	945	Republican Pub. Co.....	Advertising.....	8 70
July 6..	946	Colorado Sun.....	Advertising.....	8 70
July 30..	947	Job A. Cooper.....	Manager's compensation...	208 33
July 30..	948	Otto Mears.....	Manager's compensation...	208 33
July 30..	949	Benj. F. Crowell.....	Manager's compensation...	208 33
July 30..	950	Chas. J. Hughes, Jr.....	Manager's compensation...	208 33
July 30..	951	Peter Gumry.....	Salary as Superintendent..	300 00
July 30..	952	Thomas Mullen.....	Salary as Asst. Supt.....	200 00
July 30..	953	Herman Lueders.....	Salary as Secretary.....	166 66
Aug. 3..	954	Geddis & Seerie.....	50th Est., superstructure...	7,074 57
Aug. 3..	955	Lane Bridge and Iron Works.	14th Est., 2d contract, girders, trusses and columns..	829 89
Aug. 3..	956	Fred. Stapp.....	6th Est., slate and copper..	3,166 55
Aug. 3..	957	Frank Anderson.....	3d Est., roof sheeting.....	495 00
Aug. 3..	958	Geddis & Seerie.....	Terra cotta arches.....	2,408 00
Aug. 3..	959	Hughes & Keith S. S. Co....	Sewer pipe.....	185 00
Aug. 3..	960	Lane Bridge and Iron Works.	Material and labor.....	63 20
Aug. 3..	961	J. N. Carlile, Treasurer....	Cash advanced; paying bond coupons.....	15 00
Aug. 3..	962	Peter Gumry.....	Cash adv.; services of asst..	156 00

LIST OF VOUCHERS—Continued.

DATE.	NO.	TO WHOM PAID.	WHAT FOR.	AMOUNT.
1892.				
Aug. 3..	963	George Sebreck	Unpaid labor under W. D. Richardson	\$12 00
Aug. 3..	964	John Ryan	Unpaid labor under W. D. Richardson	11 00
Aug. 3..	965	J. D. Crable	Unpaid labor under W. D. Richardson	20 00
Aug. 3..	966	Thomas J. Scanlon	Work on Capitol grounds ..	136 00
Aug. 31..	967	Job A. Cooper	Manager's compensation...	208 34
Aug. 31..	968	Otto Mears	Manager's compensation...	208 34
Aug. 31..	969	Benj. F. Crowell	Manager's compensation...	208 34
Aug. 31..	970	Chas. J. Hughes, Jr.	Manager's compensation...	208 34
Aug. 31..	971	Peter Gumry	Salary as Superintendent ..	300 00
Aug. 31..	972	Thomas Mullen	Salary as Asst. Supt.	200 00
Aug. 31..	973	Herman Lueders	Salary as Secretary	166 67
Sept. 7..	974	Geddis & Seerie	51st Est., superstructure ...	9,156 48
Sept. 7..	975	Fred. Stapp	7th Est., slate and copper ...	1,971 89
Sept. 7..	976	Frank Anderson	4th Est., roof sheeting	1,260 00
Sept. 7..	977	Geddis & Seerie	Setting terra cotta arches ..	4,015 44
Sept. 7..	978	Geddis & Seerie	Grouting walls	136 00
Sept. 7..	979	Peter Gumry	Cash advanced; services of assistant, etc.	174 05
Sept. 7..	980	Lane Bridge and Iron Works.	Material and labor	247 11
Sept. 7..	981	Paul Reuter	Unpaid labor under W. D. Richardson	22 00
Sept. 30..	982	Job A. Cooper	Manager's compensation ...	208 33
Sept. 30..	983	Otto Mears	Manager's compensation ...	208 33
Sept. 30..	984	Benj. F. Crowell	Manager's compensation ...	208 33
Sept. 30..	985	Chas. J. Hughes, Jr.	Manager's compensation ...	208 33
Sept. 30..	986	Peter Gumry	Salary as Superintendent ...	300 00
Sept. 30..	987	Thomas Mullen	Salary as Asst. Supt.	200 00
Sept. 30..	988	Herman Lueders	Salary as Secretary	166 66
Oct. 6..	989	Geddis & Seerie	52d Est., superstructure	3,995 61
Oct. 6..	990	Lane Bridge and Iron Works.	15th Est., 2d contract, labor on dome	502 77
Oct. 6..	991	Fred. Stapp	8th Est., slate and copper work	2,178 51
Oct. 6..	992	Frank Anderson	5th Est., roof sheeting and labor	1,170 00

LIST OF VOUCHERS—Continued.

DATE.	NO.	TO WHOM PAID.	WHAT FOR.	AMOUNT.
1892.				
Oct. 6..	993	Geddis & Seerie	Setting terra cotta arches ..	\$2,326 09
Oct. 6..	994	Fred. Stapp	Cementing slate	250 00
Oct. 6..	995	Peter Gumry	Cash advanced; services of assistant, etc.	191 75
Oct. 6..	996	Colorado Telephone Co.	Office expenses, Secretary ..	20 00
Oct. 6..	997	Herman Lueders	Office expenses, Secretary ..	4 50
Oct. 31..	998	Job A. Cooper	Manager's compensation ...	208 33
Oct. 31..	999	Otto Mears	Manager's compensation ...	208 33
Oct. 31..	1000	Benj. F. Crowell	Manager's compensation ...	208 33
Oct. 31..	1001	Chas. J. Hughes, Jr.	Manager's compensation ...	208 33
Oct. 31..	1002	Peter Gumry	Salary as Superintendent ..	300 00
Oct. 31..	1003	Thomas Mullen	Salary as Asst. Supt.	200 00
Oct. 31..	1004	Herman Lueders	Salary as Secretary	166 67
Nov. 2..	1005	Geddis & Seerie	53d Est., superstructure ...	2,213 76
Nov. 2..	1006	Fred. Stapp	9th Est., slate and copper work	1,381 70
Nov. 2..	1007	Frank Anderson	6th and final Est., roof sheeting and labor	361 96
Nov. 2..	1008	Geddis & Seerie	Terra cotta arches	878 56
Nov. 2..	1009	Geddis & Seerie	Concreting floors for Superintendent's office	228 25
Nov. 2..	1010	Geo. H. Angell	Work on Capitol grounds ..	248 80
Nov. 2..	1011	Fred. Stapp	Cementing slate, etc.	153 85
Nov. 2..	1012	Colorado Iron Works	Ventilators and labor	13 84
Nov. 2..	1013	Engineering Record	Advertising proposals	24 00
Nov. 2..	1014	Engineering News Pub. Co.	Advertising proposals	18 80
Nov. 2..	1015	Republican Pub. Co.	Advertising proposals	4 35
Nov. 2..	1016	Rocky Mt. News Ptg. Co.	Advertising proposals	6 53
Nov. 2..	1017	The Colorado Sun	Advertising proposals	6 53
Nov. 2..	1018	C. J. Kelly	Printing	91 00
Nov. 2..	1019	Chain & Hardy Book, Stationery and Art Company.	Stationery, Secy's office	11 83
Nov. 2..	1020	Peter Gumry	Cash advanced; work on Capitol grounds	35 00
Nov. 2..	1021	Peter Gumry	Cash advanced; services of assistant, etc.	176 60
Nov. 2..	1022	James Fitzgerald	Unpaid labor under W. D. Richardson	487 50

LIST OF VOUCHERS—*Concluded.*

DATE.	NO.	TO WHOM PAID.	WHAT FOR.	AMOUNT.
1892.				
Nov. 2..	1023	G. A. Wood.....	Unpaid labor under W. D. Richardson	\$14 00
Nov. 9..	1024	Geddis & Seerie.....	54th Est., advance retained percentage	30,000 00
Nov. 9..	1025	Lane Bridge and Iron Wks.	16th Est., 1st Cont., advance retained per centage.....	500 00
Nov. 9..	1026	Lane Bridge and Iron Wks.	16th Est., 2d Cont., advance retained per centage.....	2,000 00
Nov. 30..	1027	Job A. Cooper	Manager's compensation...	208 34
Nov. 30..	1028	Otto Mears.....	Manager's compensation...	208 34
Nov. 30..	1029	Benj. F. Crowell	Manager's compensation...	208 34
Nov. 30..	1030	Chas. J. Hughes, Jr.	Manager's compensation...	208 34
Nov. 30..	1031	Peter Gumry.....	Salary as Superintendent ..	300 00
Nov. 30..	1032	Thomas Mullen.....	Salary as Asst. Supt.....	200 00
Nov. 30..	1033	Herman Lueders	Salary as Secretary	166 67
Total.....				\$805,133 43

DENVER, COLO., December 1, 1892.

HERMAN LUEDERS,
Secretary.

All of which is respectfully submitted.

JOHN L. ROUTT, *Chairman.*
JOB A. COOPER.
OTTO MEARS.
BENJAMIN F. CROWELL.
CHARLES J. HUGHES, JR.

APPENDIX "A."

CONTRACT FOR IRON WORK IN ATTIC FLOOR, ROOF AND ROOF CONSTRUCTION, AND PART OF DOME.

This contract, Made and entered into this 13th day of July, 1891, by and between the Board of Capitol Managers of the State of Colorado, party of the first part, and the Lane Bridge and Iron Works, of Chicago, Illinois, party of the second part:

Witnesseth, That the said Lane Bridge and Iron Works, party of the second part, for and in consideration of the covenants and agreements hereinafter mentioned, doth, for itself, its successors and assigns, covenant, promise, and agree to and with the said party of the first part, that it, the said party of the second part, will furnish all material and labor as fast as required by the Superintendent of the Capitol building, for the following classes, viz:

Class No. 1. Steel and wrought-iron work, complete;

Class No. 2. Cast-iron work, complete;

Class No. 3. Tanks in place, complete;

according to the plans, specifications and detail drawings furnished by the said Board of Capitol Managers, May 25th, 1891, to the entire satisfaction of said party of the first part, and for the sum of seventy-seven thousand nine hundred and seventy-five dollars (\$77,975), and that the said materials shall be furnished and labor performed by the said party of the second part, as aforesaid, according to the details of the following

SCHEDULE.

Schedule of quantities and prices of steel and wrought-iron work, cast-iron work, and two tanks, to be furnished and set in place, complete, at the Colorado State Capitol building, at Denver, Colorado, by the Lane Bridge and Iron Works, of Chicago, Illinois, according to the plans and specifications furnished by the Board of Capitol Managers, May 25th, 1891.

STEEL AND WROUGHT-IRON WORK.

QUANTITY, DESCRIPTION AND POSITION OF MATERIAL.	Price per 100 pounds, delivered on the ground, at the building.	Price per 100 pounds, for setting in place.	Total cost, in place, complete.
382,000 pounds of trusses and girders, in roof and over porticoes	\$5 30	\$0 20	\$21,010 00
210,000 pounds of beams, channels and connections, in ceiling	5 30	35	11,865 00
330,000 pounds of beams, channels and connections, in roof	5 45	35	19,140 00
25,900 pounds of T-iron, in ceiling and roof, not curved..	4 65	35	1,295 00
44,000 pounds of T-iron, in ceiling and roof, not curved..	6 25	35	2,904 00
151,000 pounds of beams, channels and connections, in dome, not curved	5 35	75	9,513 00
19,000 pounds of beams, channels and connections, in dome, curved	7 75	75	1,615 00
1,150 pounds of T-iron, in dome, not curved	5 25	75	69 00
15,800 pounds of T-iron, in dome, curved	7 25	75	1,264 00
Total price of steel and wrought-iron work, in place, complete			\$68,675 00

CAST-IRON WORK.

DESCRIPTION OF MATERIAL.	PRICE OF EACH ITEM.		Total cost, in place, complete.
	Delivered.	Setting, complete.	
Four columns, 8½ in. by 8½ in. by 1 in., 7 ft. 6¼ in. long....	\$28 50	\$2 50	\$124 00
Four columns, 15 in. diameter by ¾ in., 23 ft. 11 in. long....	76 00	6 00	328 00
Eight columns, 14 in. diameter by ¾ in., 16 ft. 4¼ in. long..	51 00	5 00	448 00
Four columns, 14 in. diameter by ¾ in., 12 ft. 5 in. long....	41 00	4 00	180 00
Sixteen columns, 14 in. diameter by ¾ in., 17 ft. long.....	57 00	5 00	992 00
Sixteen columns, 24 in. diameter by ¾ in., 22 ft. 5 in. long..	140 00	9 75	2,396 00
Caps and bases for the above 16 columns, 24 in. diameter, at \$22 each, in place.....			352 00
Eight columns, 24 in. diameter by ¾ in. thick, 26 ft. long...	155 00	12 00	1,336 00
Caps and bases for the above 8 columns, 24 in. diameter, at \$22 each, in place.....	13 50	1 50	176 00
Twenty-four columns, 6 in. by 6 in. by ½ in. by 3 ft. 9 in. long.	13 50	1 50	360 00
Eight columns, 15 in. diameter by ¾ in. thick by 13 ft. long.....	55 00	5 00	480 00
Caps and bases for the above 8 columns, 15 in. diameter, at \$10 each, in place.....			80 00
Eight columns, 8 in. by 8 in. by 1 in., about 8 ft. long.....	51 00	5 00	448 00
Four columns, 7 in. by 7 in. by ¾ in., 12 ft. 10½ in. long....	37 00	4 00	164 00
Two columns, 7 in. by 7 in. by ¾ in., 17 ft. 7½ in. long.....	46 00	4 00	100 00
Sixteen plates, 26 in. by 26 in. by 1½ in.....	7 00	1 50	136 00
Total cast iron work, in place, complete.....			\$8,100 00
Two tanks, each, with connections, complete, at \$600 each.....			\$1,200 00

RECAPITULATION.

Total steel and wrought-iron work, complete.....	\$68,675 00
Total cast-iron work, complete.....	8,100 00
Total tanks and connections, complete.....	1,200 00
Total contract price.....	\$77,975 00

The said party of the second part, on its part, further agrees that all of the material contracted for hereby, and to be furnished as aforesaid, shall be of the best quality, and the aforesaid directions, plans, specifications, and detail drawings of the work so contracted for as aforesaid, shall be executed by skilled and reputable artists, mechanics, and laborers.

For the considerations aforesaid, the said party of the first part, on its part, agrees to pay the said party of the second part, for the materials furnished and labor performed

as aforesaid, the said sum of seventy-seven thousand nine hundred and seventy-five dollars (\$77,975).

That said payments shall be made in parts, on monthly estimates, as per said schedule prices of work completed and of material delivered on the Capitol grounds, which said work and materials have been inspected and accepted by the said party of the first part.

It is mutually agreed, That the said party of the first part shall reserve from each of said payments on monthly estimates, as aforesaid, ten per centum thereof, until all of said work is completed, inspected and accepted, and that said reserved sum shall be due and paid when all of said work is completed, inspected, and accepted, but not otherwise.

It is further mutually agreed, That the said party of the first part has hereunder the reserved right, for good cause shown, to at any time annul this contract; and in such event, no damage shall be allowed the said party of the second part therefor, except expenses incurred and labor performed.

This contract shall take effect when, and not before, the said party of the second part shall have executed a good and sufficient bond, conditioned that this contract shall be by it faithfully performed, in the sum of twenty thousand dollars (\$20,000), signed by two securities, to be approved by the said party of the first part, each of which said securities shall be *bona fide* residents of the State of Colorado.

In witness whereof, The said parties have hereunto set their proper hands and seals, in duplicate, the day and year first above written.

THE BOARD OF CAPITOL MANAGERS.

By JOHN L. ROUTT, [SEAL]
Governor and *Ex-officio* Chairman.

LANE BRIDGE AND IRON WORKS,
P. E. LANE, *Proprietor*, [SEAL]
By WM. R. HAND, *Attorney in fact*.

Approved by order of the Board of Capitol Managers,

HERMAN LUEDEBS, *Secretary*.

BOND OF LANE BRIDGE AND IRON WORKS, CONTRACTORS.

Know all men by these presents, That the Lane Bridge and Iron Works, of Chicago, Illinois, as principals, and J. W. Nesmith and Henry C. Brown, of the State of Colorado, as securities, are held and firmly bound unto The People of the State of Colorado in the sum of twenty thousand (\$20,000) dollars, for the payment of which, well and truly to be made in the lawful money of the United States, we do bind ourselves, our heirs, executors, and administrators, jointly and severally, firmly by these presents.

Sealed with our seals and dated this 13th day of July, 1891.

The condition of the above obligation is such, That whereas the above bounden, Lane Bridge and Iron Works, did, on the 13th day of July, 1891, execute and sign a certain contract wherein the said Lane Bridge and Iron Works, as party of the second part, agreed with and promised the Board of Capitol Managers, as party of the first part, for considerations therein expressed, to furnish all labor and material at the times and according to the plans and specifications in said contract mentioned, and according to a schedule of prices, and to do and perform other things, all of which are in said contract fully set forth.

Now, therefore, If the above bounden, Lane Bridge and Iron Works, its successors, or any of them, shall well and truly perform, fulfill and keep each and all of the cove-

nants and agreements specified and contained in said contract, and pursuant to the plans and specifications therein mentioned, and the schedule of prices therein set forth; and if the Lane Bridge and Iron Works, and its successors, shall well and truly keep and perform each and every obligation, covenant and agreement which ought to be performed, fulfilled and kept, according to the true intent and meaning of said contract, then this obligation shall be void; otherwise, to remain in full force and effect.

LANE BRIDGE AND IRON WORKS,

P. E. LANE, *Proprietor*, [SEAL]
By Wm. R. HAND, *Attorney in fact*.

J. W. NESMITH. [SEAL]

HENRY C. BROWN. [SEAL]

STATE OF COLORADO, }
COUNTY OF ARAPAHOE. } ss.

J. W. Nesmith and Henry C. Brown, being first duly sworn, each for himself, upon his oath says that he is the identical J. W. Nesmith and Henry C. Brown who signed his name as one of the sureties to the bond of Lane Bridge and Iron Works, P. E. Lane, Proprietor, to which bond this affidavit is attached; that he is the owner and possessed of property in the sum of twenty thousand dollars (\$20,000) over and above all liabilities, debts, incumbrances and exemptions allowed by the law of the State of Colorado.

J. W. NESMITH.
HENRY C. BROWN.

Subscribed and sworn to before me, this 13th day of July, A. D. 1891.

PERCY AUSTIN, *Notary Public*.

My commission expires March 16th, 1892.

Approved July 13th, 1891.

JOHN L. ROUTT, Governor,
Chairman of the Board of Capitol Managers.

ATTEST: HERMAN LUEDERS, *Secretary*.

APPENDIX "B."

CONTRACT FOR SLATE AND SLATE WORK, GALVANIZED IRON AND COPPER WORK, AND SKYLIGHT IN ROOF, COMPLETE.

This contract, Made and entered into this 17th day of July, 1891, by and between the State Board of Capitol Managers, of the State of Colorado, party of the first part, and Frederick Stapp, of the City of Denver and of the State of Colorado, party of the second part:

Witnesseth, That for and in consideration of the covenants and agreements herein-after mentioned, the said party of the second part doth covenant, promise and agree, to and with the said party of the first part, that he, the said party of the second part, will furnish all material and labor as fast as required by the Superintendent of the Capitol building, now in process of erection in the City of Denver, for the following classes, viz:

Class No. 4. Slate and slate work, complete;

Class No. 5. Galvanized iron and copper work, complete;

Class No. 6. Skylight in roof, complete;

according to the plans and specifications furnished by the said Board of Capitol Managers, May 25th, 1891, to the entire satisfaction of the said party of the first part, for the

sum of twenty-five thousand and sixty-one dollars (\$25,061.00), and that said materials shall be furnished and labor performed by the said party of the second part, as aforesaid, according to the details of the following

SCHEDULE.

Schedule of quantities and prices furnished by Frederick Stapp, for the slate and slate work, galvanized iron and copper work, and skylights, as per plans, specifications and detail drawings furnished by the Board of Capitol Managers, May 25th, 1891, also as per samples on file with the Board.

SLATE AND SLATE WORK.

Slate work, complete (507 squares, \$36.37 per sq.) in the building.....	\$18,443 00
507 squares of slate (94 slate to the square), \$24.50 per square, on the ground.....	\$12,421 50
12,675 square yards of asbestos paper, 10½ cents per square yard, on the ground.....	1,330 83
566 gross of brass screws, \$1.50 per gross, on the ground.....	849 00
Oiling 507 squares of slate, \$2.25 per square.....	1,140 75
Laying 507 squares of slate, including the laying of paper, putty and screws, \$5 ³² / ₁₀₀₀ per square.....	2,700 87
Class No. 4—Total slate work, complete.....	\$18,443 00

GALVANIZED IRON AND COPPER WORK.

Copper and galvanized iron work complete, in the building.....	\$4,885 00
1,072 lineal feet of copper gutter, \$1.20 per foot, on the ground....	\$1,286 40
Laying same in place, 4.06 cents per foot.....	436 00
672 lineal feet of hip roll, 50 cents per foot, on the ground.....	336 00
Laying same in place, 5 cents per foot.....	33 60
832 feet of valleys, 50 cents per foot, delivered on the ground....	416 00
Laying same in place, 5 cents per foot.....	41 60
468 lineal feet of ridge comb, 60 cents per foot, delivered on the ground.....	280 80
Laying same in place, 10 cents per foot.....	46 80
11 copper ventilating pipes, \$5 each, delivered on the ground....	55 00
Setting same in place, \$3 each.....	33 00
1 galvanized iron flag-pole, delivered on the ground.....	75 00
Setting flag-pole in place.....	50 00
575 square feet of copper roofing, delivered on ground.....	249 55
Laying same.....	74 75
1,600 copper flashing, delivered on the ground.....	425 00
Laying same in place.....	125 00
6 galvanized iron ventilating stacks, delivered on the ground....	450 00
Setting same in place.....	150 00
1 smoke stack cap, delivered on the ground.....	200 00
Setting same in place.....	90 50
Class No. 5—Copper and galvanized iron work, complete.....	\$4,855 00

Skylight in roof, complete.....	\$1,763 00
1763 square feet of skylight glass, delivered on the ground.....	\$1,200 00
Laying same in place.....	563 00
Class No. 6—Total, skylights in place, complete.....	\$1,763 00

The said party of the second part further agrees and promises, that all material contracted for hereby, and to be furnished as aforesaid, shall be of the best quality, and the aforesaid directions, plans and specifications shall be executed by skilled and reputable artists, mechanics, and laborers.

For the considerations aforesaid, the said party of the first part, on its part, agrees to pay the said party of the second part, for the materials furnished and labor performed, as aforesaid, the said sum of twenty-five thousand and sixty-one dollars (\$25,061.00); and that said payments shall be made in parts on monthly estimates, as per said schedule prices, or work completed and materials delivered on the Capitol grounds, which said work and materials shall have been first inspected and accepted by the said party of the first part.

It is mutually agreed, That the said party of the second part shall reserve from each of said payments on monthly estimates, as aforesaid, ten per centum thereof, until all of said work is completed, inspected and accepted by the said party of the first part, and that said reserved sum shall be due and paid when all of said work is so completed, inspected and accepted, but not otherwise.

It is further mutually agreed, That the said party of the first part has hereunder reserved the right, for good cause shown, to at any time annul this contract; and in such event, no damage shall be allowed the said party of the second part therefor, except expenses incurred and labor performed.

This contract shall take effect when, and not before, the said party of the second part shall have executed a good and sufficient bond, conditioned that this contract shall be faithfully performed, in the sum of sixty-five hundred dollars (\$6,500.00), signed by one or more securities, who are *bona fide* residents of the State of Colorado, and who shall be approved by the said party of the first part.

In witness whereof, The said parties have hereunto set their proper hands and seals, in duplicate, the day and year first above written.

THE BOARD OF CAPITOL MANAGERS,

By JOHN L. ROUNTT, [SEAL]
Governor and Ex-officio Chairman.

FREDERICK STAPP. [SEAL]

Approved by order of the Board of Capitol Managers.

HERMAN LUEDERS, *Secretary.*

BOND OF FREDERICK STAPP, CONTRACTOR.

Know all men by these presents, That we, Frederick Stapp, as principal, and E. F. Hallack and H. W. Michael, as sureties, all of the City of Denver, County of Arapahoe and State of Colorado, are held and firmly bound unto The People of the State of Colorado, in the sum of sixty-five hundred dollars (\$6,500.00), good and lawful money of the United States, to be paid to the said The People of the State of Colorado, or their assigns; for which payment, well and truly to be made, we do bind ourselves, our heirs, executors and administrators, jointly and severally, firmly by these presents.

Signed and sealed this 14th day of July, 1891.

The condition of the above obligation is such, That whereas, the above bounden, Frederick Stapp, as party of the second part, and the Board of Capitol Managers, acting for and in behalf of the said The People of the State of Colorado, by virtue and in pursuance of an act entitled "An act to provide for the erection and completion of a State Capitol building, at the City of Denver, and creating a Board of Management and Supervision," approved April 1, 1889, as party of the first part, did, on June 16,

1891, execute and sign a certain contract, the object and intent of said contract being, among other things, to bind and obligate the said Frederick Stapp, for considerations therein named, to furnish all materials and labor as fast as required by the Superintendent of said Capitol building, now in process of erection in the City of Denver, for the following classes, viz:

- Class No. 4. Slate and slate work, complete;
- Class No. 5. Galvanized iron and copper work, complete;
- Class No. 6. Skylight in roof, complete;

according to certain terms, plans and specifications in said contract named and set forth.

Now, If the above bounden, Frederick Stapp, his executors and administrators, or any of them, shall well and truly perform, keep and fulfill each and all of the covenants and agreements specified and contained in the contract aforesaid, and if the said Frederick Stapp, his executors and administrators, or any of them, shall well and truly keep and perform each and every obligation, covenant and agreement which ought to be performed, kept and fulfilled, according to the terms, intent and meaning of said contract, then the above obligation shall be void; otherwise, to remain in full force and effect.

FREDERICK STAPP. [SEAL]

E. F. HALLACK. [SEAL]

H. W. MICHAEL. [SEAL]

STATE OF COLORADO, }
COUNTY OF ARAPAHOE, } ss.

E. F. Hallack and H. W. Michael, being first duly sworn, each for himself, upon his oath says, that he is the identical E. F. Hallack and H. W. Michael who signed his name as one of the sureties to the bond of Frederick Stapp, to which bond this affidavit is attached; that he is the owner and possessed of property in the sum of sixty-five hundred dollars (\$6,500.00), over and above all liabilities, debts, incumbrances and exemptions allowed by the laws of the State of Colorado.

E. F. HALLACK. [SEAL]

H. W. MICHAEL. [SEAL]

Sworn to and acknowledged before me, this 14th day of July, 1892.

W. H. WOLFERSBERGER, *Notary Public.*

My commission expires February 17th, 1892.

Approved July 17th, 1892.

JOHN L. ROUNTT, Governor,
Ex-officio Chairman Board of Capitol Managers.

ATTEST: HERMAN LUEDERS, *Secretary.*

APPENDIX "C."

ROOF CONSTRUCTION.

CONTRACT FOR MATERIAL AND CARPENTER WORK, COMPLETE.

This contract, Made and entered into this 7th day of August, 1891, by and between the State Board of Capitol Managers of the State of Colorado, party of the first part, and Frank Anderson, of the City of Denver and State of Colorado, party of the second part:

Witnesseth, That the said party of the second part, for and in consideration of the covenants and agreements hereinafter mentioned, doth for himself, his executors and administrators, covenant, promise, and agree to and with the said party of the first part, that he, the said party of the second part, will furnish all labor and material as fast as required by the Superintendent of the Capitol building, now in process of erection in said city of Denver, for carpenter work complete, according to the plans and specifications furnished by the said Board of Capitol Managers, May 25th, 1891, to the entire satisfaction of the said party of the first part, and for the sum of six thousand one hundred dollars (\$6,100), and that the said materials shall be furnished and labor performed by the said party of the second part, as aforesaid, according to the details of the following

SCHEDULE.

Schedule of quantities and prices of carpenter work to be furnished and put in place, complete, at the Colorado State Capitol building, at Denver, Colorado, by Frank Anderson, of Denver, Colorado, according to the plans, specifications and detail drawings furnished by the Board of Capitol Managers, May 25th, 1891.

DESCRIPTION AND QUANTITIES OF MATERIAL.	Price per 1,000 ft., B. M., delivered at the building.	Price per 1,000 ft., B. M., for erection.	Total price, in place, complete.
3,000 feet, B. M., 1 inch Oregon gutter boards, at \$40 per 1,000	\$120 00	\$16 66%	\$170 00
4,500 feet, B. M., 2 inches by 4 inches and 2 in. by 6 in., Oregon rafters and purlins, at \$30 per 1,000	1,350 00	20 00	2,250 00
90,000 feet, B. M., 1½ inches by 4 inches, Oregon sheathing, tongued and grooved, at \$35 per 1,000	3,150 00	5 89	3,680 00
Total carpenter work, complete.....			\$6,100 00

The said party of the second part further agrees and promises, that all of the material contracted for hereby, and to be furnished as aforesaid, shall be of the best quality and the aforesaid directions, plans, and specifications shall be executed by skilled and reputable artists, mechanics, and laborers.

For the considerations aforesaid, the said party of the first part, on its part, agrees to pay the said party of the second part, for the materials furnished and labor performed, as aforesaid, the said sum of six thousand one hundred dollars (\$6,100), and that said payments shall be made in parts, on monthly estimates, as per said schedule

prices of work completed and materials delivered on the Capitol grounds, which said work and materials shall have been first inspected and accepted by the said party of the first part.

It is mutually agreed, That said party of the second part shall reserve from each of said payments on monthly estimates, as aforesaid, ten per centum thereof until all of said work is completed, inspected and accepted by the said party of the first part, and that said reserved sum shall be due and paid when all of said work is so completed, inspected, and accepted, but not otherwise.

It is further mutually agreed, That the said party of the first part has hereunder the reserved right to at any time, for good cause shown, annul this contract, and in such event, no damage shall be allowed the said party of the second part therefor, except expenses incurred and labor performed.

This contract shall take effect when, and not before, the said party of the second part shall have executed a good and sufficient bond, conditioned that this contract shall be faithfully performed, in the sum of one thousand six hundred dollars (\$1,600), signed by one or more securities, who are *bona fide* residents of the State of Colorado, and who shall be approved by the said party of the first part.

In witness whereof, The said parties have hereunto set their proper hands and seals, in duplicate, the day and year first above written.

THE BOARD OF CAPITOL MANAGERS,

By JOHN L. ROUNT, [SEAL]

Governor and Ex-officio Chairman.

FRANK ANDERSON. [SEAL]

Approved by order of the Board of Capitol Managers.

HERMAN LUEDERS, *Secretary*.

BOND OF FRANK ANDERSON, CONTRACTOR.

Know all men by these presents, That we, Frank Anderson, as principal, and Fine P. Ernest and Philip Feldhauser, as sureties, all of the City of Denver, County of Arapahoe, and State of Colorado, are held and firmly bound unto The People of the State of Colorado in the sum of one thousand six hundred dollars (\$1,600), good and lawful money of the United States, to be paid to the said The People of the State of Colorado, or their assigns, for which payment, well and truly to be made, we do bind ourselves, our heirs, executors, and administrators, jointly and severally, firmly by these presents.

Signed and sealed this first day of August, 1891.

The condition of the above obligation is such, That whereas, the above bounden, Frank Anderson, as party of the second part, and the Board of Capitol Managers, acting for and in behalf of the said The People of the State of Colorado, by virtue and in pursuance of an act entitled "An act to provide for the erection and completion of a State Capitol building at the City of Denver, and creating a Board of Management and Supervision," approved April 1st, 1889, as party of the first part, did execute and sign a certain contract, the object and intent of said contract being, among other things, to bind and obligate the said Frank Anderson, for considerations therein named, to furnish all materials and labor for carpenter work, complete, for the said Capitol building now in process of erection in the City of Denver, according to certain terms, plans, and specifications in said contract named and set forth.

Now, if the above bounden, Frank Anderson, his executors and administrators, or any of them, shall well and truly perform, keep, and fulfill each and all of the covenants and agreements specified and contained in the contract aforesaid, and if the said

Frank Anderson, his executors and administrators, or any of them, shall well and truly keep and perform each and every obligation, covenant and agreement which ought to be performed, kept, and fulfilled, according to the terms, intent, and meaning of said contract, then the above obligation shall be void; otherwise, to remain in full force and effect.

FRANK ANDERSON. [SEAL]

FINE P. ERNEST. [SEAL]

PHILIP FELDHAUSER. [SEAL]

STATE OF COLORADO, }
COUNTY OF ARAPAHOE. } ss.

Fine P. Ernest and Philip Feldhauser, being first duly sworn, each for himself, upon his oath says, that he is the identical Fine P. Ernest and Philip Feldhauser who signed his name as one of the sureties to the bond of Frank Anderson, to which bond this affidavit is attached; that he is the owner and possessed of property in the sum of sixteen hundred dollars (\$1,600) over and above all liabilities, debts, incumbrances and exemptions allowed by the laws of the State of Colorado.

FINE P. ERNEST.

PHILIP FELDHAUSER.

Subscribed and sworn to before me this first day of August, A. D. 1891.

WILLIAM E. WHITE, *Notary Public.*

My commission expires June 5th, 1895.

Approved August 7th, 1891.

JOHN L. ROUTT, Governor,
Ex-officio Chairman, Board of Capitol Managers.

Attest: HERMAN LUEDERS, *Secretary.*

APPENDIX "D."

CONTRACT FOR ROOF DRAINAGE.

This contract, Made and entered into this 6th day of January, 1892, by and between the State Board of Capitol Managers of the State of Colorado, party of the first part, and Geddis & Seerie, a co-partnership composed of William Ford Geddis and David Duff Seerie, of the City of Denver, State of Colorado, party of the second part:

Witnesseth, That the said parties of the second part, for and in consideration of the agreements hereinafter mentioned, to be kept and performed by the said party of the first part, do, for themselves, their heirs, executors and administrators, covenant, promise and agree, to and with the said party of the first part:

First—That they will do all the work and furnish all the materials for the roof drainage of the Capitol building of said State, now in process of erection, in accordance with the drawings, plans and specifications in relation thereto, on file in the office of P. Gumry, superintendent of construction of said Capitol building, at the Capitol grounds, in the said City of Denver, for the sum of two thousand dollars (\$2,000.00), and that said contract will be performed as ordered by the Superintendent.

Second—That all the material used in the fulfillment of this contract shall be of the best quality, and the directions, plans and specifications of the work shall be executed by skilled and reputable contractors, artists, mechanics, and laborers.

Third—That the said parties of the first part shall have the right, for good cause shown, to annul this contract; and in such event, the said party of the first part shall make no allowance for damages, only for expenses incurred and labor performed.

Fourth—That not less than ten per cent. shall be reserved by the party of the first part, from payments on monthly estimates on work herein contracted for, until all of such work shall have been completed, inspected by the Superintendent, and accepted by the said party of the first part.

The said party of the first part, in consideration of the covenants, promises and agreements hereinbefore contained, promises and agrees to pay the said party of the second part, for the work done and materials furnished, as hereinbefore specified, when inspected and accepted as aforesaid, the aforesaid sum of two thousand dollars (\$2,000.00), by voucher issued to the State Auditor, certifying that the said services have been rendered, and that the owner thereof is entitled to a warrant on the State Treasurer for the amount therein named, against the "Capitol Building fund," and that said payments may, if desired by the party of the second part, be paid in installments on monthly estimates, with ten per cent. reserved, as hereinbefore set forth, the balance due at the completion of this contract, with the said amount reserved, to be paid as aforesaid, when the work has been accepted as aforesaid.

It is mutually understood, That this contract is made pursuant to an act of the Fifth General Assembly of the State of Colorado, entitled "An act to provide for the erection and completion of a State Capitol building at the City of Denver, and creating a Board of Management and Supervision," approved April 1, 1889, and that the provisions of said act control where the terms of this contract, if any, are in conflict therewith, and in all particulars in which this contract is silent.

In witness whereof, The parties hereto have hereunto set their hands and seals, at the City of Denver, the day and year first above written.

THE BOARD OF CAPITOL MANAGERS,
By JOHN L. ROUTT, [SEAL]
Governor, and Chairman of the Board.

WILLIAM F. GEDDIS. [SEAL]
DAVID D. SEERIE. [SEAL]

Approved by order of the Board of Capitol Managers.

HERMAN LUEDERS, *Secretary.*

BOND OF GEDDIS & SEERIE.

Know all men by these presents, That the undersigned, Geddis & Seerie, a co-partnership, of the City of Denver, State of Colorado, composed of William Ford Geddis and David Duff Seerie, as principal, and George N. Steinmetz and Edward R. Ball, as sureties, are held and firmly bound unto The People of the State of Colorado, in the sum of five hundred dollars (\$500.00), for the payment of which, in lawful money of the United States, well and truly to be made, we bind ourselves, our heirs, executors and administrators, jointly and severally, firmly by these presents.

Signed and sealed this 6th day of January, A. D. 1892.

The conditions of the above obligation are such, That whereas, the above bounden, Geddis & Seerie, have entered into a contract, of even date herewith, whereby they have

promised and agreed with the State Board of Capitol Managers to do all the work and furnish all the materials for the roof drainage of the State Capitol building, now in process of erection in the City of Denver, in accordance with certain plans and specifications, and for a compensation in said contract designated.

Now, If the said Geddis & Seerie shall fully and faithfully perform said contract, in each and every particular, then this obligation is to be void; otherwise, to remain in full force and effect.

WILLIAM F. GEDDIS. [SEAL]
 DAVID D. SEERIE. [SEAL]
 GEORGE N. STEINMETZ. [SEAL]
 EDWARD R. BALL. [SEAL]

STATE OF COLORADO, }
 COUNTY OF ARAPAHOE, } ss.

George N. Steinmetz and Edward R. Ball, being duly sworn, depose and say, each for himself, that he is the identical George N. Steinmetz and Edward R. Ball, who signed his name as one of the sureties on the bond of William Ford Geddis and David D. Seerie, to which this affidavit is attached; that he is the owner and possessed in the State of Colorado, in the sum of five hundred dollars (\$500.00) over and above all liabilities, incumbrances and exemptions allowed by the laws of Colorado.

GEORGE N. STEINMETZ.
 EDWARD R. BALL.

Subscribed and sworn to before me this 16th day of March, 1892.

CHESTER D. BARNES, *Notary Public.*

My commission expires March 1st, 1894.

Approved, JOHN L. ROUTT, Governor,
Chairman of the Board of Capitol Managers.

ATTEST: HERMAN LUEDERS, *Secretary.*

APPENDIX "E."

CONTRACT FOR GRADING GROUNDS.

This agreement, Made and entered into this 25th day of May, A. D. 1892, by and between the State Board of Capitol Managers of the State of Colorado, party of the first part, and Thomas C. Scanlon, of the City of Denver, party of the second part,

WITNESSETH: *First*—That the said party of the first part hereby employs the said party of the second part, to grade all that part of the State Capitol grounds lying west of the west front of the Capitol building.

Second—The party of the second part, in consideration of the agreements herein contained, and the payment of the sum of money hereinafter named, agrees to execute and remove the dirt on said grounds, under the direction of the engineer in charge acting for said Board; said grounds to be graded and filled according to the plat and profile of established grades hereto attached, commencing on the side next to Colfax avenue, and proceeding south, and continuously completing the surface as he proceeds,

so that what is completed will be all together, and the uncompleted part, if any, will be in the southwest corner of said grounds. The grading and filling shall both be left in a smooth and perfect grade; all stone or objectionable material shall be removed or covered up. The grounds shall be left completed, as above stated, according to the said established grades, and shall be satisfactory to the engineer in charge. The said engineer shall have full direction and supervision of the work, and decide whether or not it is done according to this agreement.

Third—This contract is for the entire work, without reference to the amount of dirt to be removed; and the said party of the second part agrees to complete said work, as aforesaid, within thirty working days from the date hereof.

Fourth—The party of the second part further agrees to make full payment to all his employes for any and all work done by them in the performance of this contract, and to execute his bond, of even date herewith, in the sum of twelve hundred dollars (\$1,200.00), with sureties, to be approved by said Board, for the faithful performance of all his promises and agreements herein contained.

Fifth—The party of the first part, in consideration of the premises, promises and agrees, that when the aforesaid work is completed, according to the aforesaid specifications and according to the aforesaid plat and profile of established grades, hereto attached, which are made a part of this contract, and shall be approved by said engineer, to pay the said party of the second part therefor the sum of one thousand one hundred and forty-three dollars (\$1,143.00), by voucher, as the law in such cases provides.

Signed in duplicate, the day and year first above written, the party of the first part, pursuant to its order heretofore made, signing by its president.

THE BOARD OF CAPITOL MANAGERS,

By JOHN L. ROUTT, [SEAL]
Governor and Chairman of the Board.

THOMAS C. SCANLON. [SEAL]

Approved by order of the Board of Capitol Managers.

HERMAN LUEDERS, *Secretary.*

BOND OF THOMAS C. SCANLON.

Know all men by these presents, That we, Thomas C. Scanlon, as principal, and Bernard M. Slack and E. R. Barton, as sureties, are held and firmly bound unto The People of the State of Colorado, in the sum of \$1,200, for the payment of which, well and truly to be made, we hereby bind ourselves, our heirs, executors, firmly by these presents.

Signed and sealed this 25th day of May, A. D. 1892.

The condition of this obligation is such, That whereas, the above bounden, Thomas C. Scanlon, has this day entered into a contract with the State Board of Capitol Managers of said State of Colorado, whereby he agrees to grade all that part of the State Capitol grounds lying west of the west front of the Capitol building.

Now, If the said Thomas C. Scanlon shall well and truly perform all his agreements and promises in said contract contained, to the satisfaction of said Board, and upon the acceptance of its engineer in said contract mentioned, and within the time named in said contract, then this obligation is to be void; otherwise, to remain in full force and effect.

THOMAS C. SCANLON. [SEAL]
 BERNARD M. SLACK. [SEAL]
 E. R. BARTON. [SEAL]

STATE OF COLORADO, }
ARAPAHOE COUNTY, } ss.

Bernard M. Slack and E. R. Barton, being duly sworn, depose and say, each for himself, that he is the identical Bernard M. Slack and E. R. Barton, who signed his name as one of the sureties on the bond of Thomas C. Scanlon, to which this affidavit is attached; that he is the owner and possessed in the State of Colorado in the sum of twelve hundred dollars (\$1,200.00), over and above all liabilities, incumbrances and exemptions allowed by the laws of Colorado.

BERNARD M. SLACK,
E. R. BARTON.

Subscribed and sworn to before me, this 25th day of May, A. D. 1892.

ORTA E. ADAMS, *Notary Public.*

My commission expires November 21st, 1893.

Approved: JOHN L. ROUTT, Governor,
Chairman of the Board of Capitol Managers.

ATTEST: HERMAN LUEDERS, *Secretary.*

APPENDIX "F."

CONTRACT FOR ENCLOSING THE BUILDING.

This contract, Made and entered into this 24th day of September, 1892, by and between the State Board of Capitol Managers of the State of Colorado, party of the first part, and Frank Anderson, of the City of Denver, said State, party of the second part:

Witnesseth, That the said party of the first part, having heretofore accepted the bid of the said party of the second part, to temporarily enclose the State Capitol building, the said party of the second part, in consideration of the premises, and of the promises and agreements hereinafter contained, on his part promises and agrees:

First—To furnish all material for and labor required to temporarily enclose the said State Capitol building, by closing the doors and windows of the same, according to the plans and specifications furnished by the Superintendent of said building, viz, Peter Gumry, and for the following prices, respectively, to wit:

(a) To put floors in one room 32x40, and in one room 11x11, for the sum of..	\$88 25
(b) To enclose windows, as follows:	
Basement windows, without glass, each	1 65
First story windows, without glass, each	2 75
Second story windows, without glass, each	3 00
Third story windows, without glass, each	2 35
(c) Doors not hung, each	3 40
(d) Doors, if hung, each	4 50
And for windows 10x14x12, each.....	2 16
Amounting in all to the sum of.....	1,314 00

Second—To perform this contract within sixty days from the date hereof, and the same shall be subject to the approval and acceptance of the Superintendent in charge for the party of the first part.

Third—To execute his bond, of even date herewith, in the sum of seven hundred (\$700) dollars, for the faithful performance of this contract, signed by two sureties, to be approved by the Board, each of whom shall be a bona fide resident of the State of Colorado.

The said party of the first part, on its part, promises and agrees to pay the said party of the second part, for and upon his faithful performance of his part of this agreement, within sixty days of the date hereof, the sum of one thousand three hundred and fourteen (\$1,314) dollars, by voucher, as provided by law.

The party of the first part reserves the right, for good cause shown, to annul this contract; in such event, no allowance for damages, except for expenses incurred and for labor performed, shall be made.

It is mutually understood and agreed between the parties hereto, that this contract is made pursuant to "An act to provide for the erection and completion of the State Capitol building," etc., approved April 1st, 1889, and that the provisions of said act shall control in all particulars, if any, in which this contract is in conflict therewith, or in which it is silent.

In witness whereof, The said parties hereto have duly executed this contract, the day and year first above written.

THE BOARD OF CAPITOL MANAGERS,

By JOHN L. ROUTT, Governor, [SEAL]

Ex-officio Chairman of the Board.

FRANK ANDERSON.

[SEAL]

Approved by order of the Board of Capitol Managers.

HERMAN LUEDERS, *Secretary.*

BOND OF FRANK ANDERSON.

Know all men by these presents, That we, Frank Anderson, of the City of Denver, State of Colorado, as principal, and C. E. Rohrer and C. D. McPhee, as sureties, bona fide residents of the State of Colorado, are held and firmly bound unto the State of Colorado in the sum of seven hundred (\$700) dollars, for the payment of which, well and truly to be made, we bind ourselves, our heirs, executors, and administrators, firmly by these presents.

Signed and sealed this 24th day of September, 1892.

The condition of this obligation is such, That whereas the above bounden, Frank Anderson, has entered into an agreement, of even date herewith, with the State Board of Capitol Managers, for the temporary enclosing of the State Capitol building, which said contract is hereto attached.

Now, therefore, If the said Frank Anderson shall well and truly perform said contract in every particular, to the satisfaction of said Board of Capitol Managers, then this obligation is to be void; otherwise, to remain in full force and effect.

FRANK ANDERSON. [SEAL]

C. D. MCPHEE. [SEAL]

C. E. ROHRER. [SEAL]

STATE OF COLORADO, }
 COUNTY OF ARAPAHOE. } ss.

C. E. Rohrer and Charles D. McPhee, being duly sworn according to law, each for himself on his oath states that he is a *bona fide* resident of the State of Colorado, and that he is worth seven hundred (\$700) dollars over and above his statutory exemptions.

C. E. ROHRER.

CHARLES D. MCPHEE.

Subscribed and sworn to before me, this 24th day of September, A. D. 1892.

WILLIAM E. WHITE, *Notary Public*.

My commission expires June 5th, 1895.

Approved:

JOHN L. ROUNTT, Governor,
Ex-officio Chairman Board of Capitol Managers.

Attest: HERMAN LUEDERS, *Secretary*.

APPENDIX "G."

ACTS

OF THE

EIGHTH GENERAL ASSEMBLY

OF THE STATE OF COLORADO.

AN ACT

TO PROVIDE FOR THE CREATION OF AN ADDITIONAL BONDED INDEBTEDNESS BY THE STATE, TO THE AMOUNT OF THREE HUNDRED THOUSAND DOLLARS, TO AID IN THE CONSTRUCTION OF THE STATE CAPITOL BUILDING.

Be it enacted by the General Assembly of the State of Colorado:

SECTION 1. There shall be submitted to the vote of the qualified electors of the State of Colorado, at the general election occurring in November, 1891, for their ratification or rejection, a proposition to create a bonded indebtedness of the State, to the amount of three hundred thousand dollars, the same to be additional to the indebtedness of three hundred thousand dollars heretofore authorized by the qualified electors, under an act approved February 11, 1883, the bonds representing such indebtedness to be due and payable in fifteen years from the date of issue, and to bear interest at a rate not exceeding four per cent. per annum, and not to be sold for less than their par value, the proceeds thereof to be used in the construction of the State Capitol building.

SEC. 2. The Secretary of State shall, at least thirty days prior to said general election, make out and cause to be delivered to the county clerk of each county in the State a notice, in writing, stating that at such general election the question of voting said bonded indebtedness will be submitted to a vote of the qualified electors of the State; and the county clerk of each county shall thereupon give notice in writing of such election, and by causing the same to be published in a newspaper having general circulation in the county, and sending a copy of such notice by mail to the judges of election in each precinct, to be posted at the place of voting at least fifteen days before the date of said election.

SEC. 3. All persons voting on the question shall vote by separate ballot, which shall be deposited in a box to be used for that purpose only, on which ballot shall be printed the words, "For the creation of an additional bonded indebtedness of three hundred thousand dollars to aid in the erection of a State Capitol building;" or, "Against the creation of an additional bonded indebtedness of three hundred thousand dollars to aid in the erection of a State Capitol building." The vote so cast on the question of the creation of said bonded indebtedness shall be canvassed and the result determined in the same manner as provided by the laws of this State for the canvass and return of representatives in Congress.

SEC. 4. The board of commissioners of the State debt, as created by an act of the General Assembly, entitled "An act to provide for the creation of a bonded indebtedness on behalf of the State, to the amount of three hundred thousand dollars, to aid in the construction of a State Capitol building in the City of Denver, and for the submis-

sion of the question to a vote of the qualified electors of the State," approved February 11, 1883, shall have a like power and authority in respect to said additional bonded indebtedness as by said act was conferred upon said board in respect to the bonded indebtedness of three hundred thousand dollars, as created by said act and the ratification thereof by the qualified electors of the State of Colorado. If a majority of the votes lawfully cast shall be in favor of the creation of such indebtedness, then said board of commissioners shall proceed to carry out the provisions of this act by the issue of coupon bonds of the State of Colorado, as hereinafter set forth; the bonds issued shall be comprised in one series of three hundred bonds, numbered from number one to number three hundred, both numbers inclusive, to be of the denomination of one thousand dollars each, with interest at a rate to be determined by said board, but not to exceed four per cent. per annum, to be evidenced by coupons attached to said bonds, and to be paid semi-annually at the office of the State Treasurer, at the City of Denver, or at such bank or banking house in the City of New York, as said board may designate. The principal of said bonds shall be due and payable in fifteen years from date of issue, at the office of the State Treasurer. All the bonds issued under this act shall be registered in the office of the State Auditor, and his certificate of such registry and the seal of his office shall be affixed to each bond, which certificate and seal shall be evidence of their legal issue.

SEC. 5. The bonds issued under this act shall be known as "Capitol-Building Bonds, Second Series," and shall be signed by the Governor of the State, countersigned by the State Treasurer and attested by the Secretary of State, who shall affix the great seal of the State to each bond. They shall be numbered and registered in a book kept for that purpose by the State Treasurer, in the order in which they are issued. Each bond shall state upon its face the amount for which it is issued, to whom issued, for what purpose issued, the date of its issue and the title of this act, the text of which shall be printed on the reverse side of each bond.

SEC. 6. Whenever the bonds are issued, as provided in this act, it shall be the duty of the State board of equalization to levy and assess a special tax on all the taxable property in the State, sufficient in amount to discharge the interest accruing thereon, and payable half yearly; which tax, when collected, shall [be] paid into the State treasury to the credit of the interest fund. And, for the ultimate redemption of said bonds, there shall be levied annually for five years, after nine years from the date of their issue, such tax upon all the taxable property in the State as shall create a yearly fund equal to twenty per cent. of the whole amount of the bonds issued; which fund shall be called "The Capitol-Building Bond Sinking Fund," and all taxes for interest on and for the redemption of such bonds, shall be levied and collected as other State taxes, and shall be paid into the State treasury in cash only. The proceeds thereof shall be kept by the State Treasurer as special and distinct funds, under their respective heads, to be used in payment of interest on and for the redemption of such bonds only, or for their purchase, as hereinafter provided, and for no other purpose whatever: *Provided*, That whenever any surplus remains to the credit of the interest fund after the full payment of the interest maturing in any year, the said board of commissioners shall cause such surplus to be transferred to the credit of the "Capitol-Building Bond Sinking Fund." All moneys belonging to the said sinking fund may be invested by said board of commissioners in such of the Capitol-building bonds, issued by virtue of the act of the General Assembly, approved February, 1883, providing for the creation of a bonded indebtedness in behalf of the State, to the amount of three hundred thousand dollars, to aid in the construction of a Capitol building in the City of Denver, and of those issued under and by virtue of the provisions of this act, and also in any other bonds lawfully issued by this State, as may be obtainable, or in the registered bonds of the United States, as in the judgment of said board may best serve the interests of the State. The said board of commissioners of the State debt shall, whenever called upon, report to the General Assembly the condition of said sinking fund and the amount of the same, and how invested.

SEC. 7. For the payment of the coupons representing the first year's interest accruing on the bonds to be issued under this act, the State Treasurer is hereby authorized and directed to apply any moneys at that time in his hands belonging to the Capitol-building fund, such moneys so used to be restored by him to the said fund, by transfer from the interest fund, as soon as a sufficient amount is received into the said interest fund from the collection of interest tax, as hereinbefore provided.

SEC. 8. When any of the bonds issued under this act are purchased or redeemed, it shall be the duty of said board of commissioners to cancel the same, so that they can be plainly identified, and cause the record of such cancellation to be made on the bond registry books of the State Treasurer and State Auditor.

SEC. 9. The said board of commissioners shall be authorized to prescribe the form of the bonds to be issued under this act, and of the coupons thereto; and when said issue is made, as hereinbefore provided, the board shall be authorized to dispose of the same for cash, not less than par, and deposit the proceeds thereof with the State Treasurer to the credit of the Capitol-building fund, to be used to aid in the erection of a Capitol building for the State of Colorado, in such manner as may be provided by the acts of the General Assembly.

SEC. 10. This act shall not be revised, amended or repealed until the total amount of the indebtedness herein provided for is fully paid and discharged.

Approved March 26, 1891.

AN ACT

TO TRANSFER AND APPROPRIATE THE FUNDS NOW TO THE CREDIT OF THE PUBLIC BUILDING INCOME FUND AND THE PUBLIC BUILDING LAND PERMANENT FUND TO THE CREDIT OF THE CAPITOL BUILDING FUND.

Be it enacted by the General Assembly of the State of Colorado:

SECTION 1. The entire sum now standing to the credit of those certain funds known as and designated the public building income fund and the public building land permanent fund, together with such further sums of money as may, during the years 1891 and 1892, be paid in to the credit of said several funds, are hereby transferred and appropriated to the Capitol-building fund, for the purpose of aiding in the construction of the State Capitol building.

SEC. 2. In the opinion of [the] General Assembly an emergency exists; and therefore, this act shall take effect and be in force from and after its passage.

Approved April 1, 1891.

AN ACT

FOR THE TRANSFER AND LOAN OF ONE HUNDRED AND FIFTY THOUSAND DOLLARS FROM THE INTERNAL IMPROVEMENT PERMANENT FUND TO THE CAPITOL BUILDING FUND.

Be it enacted by the General Assembly of the State of Colorado:

SECTION 1. There shall be transferred from the internal improvement permanent fund to the Capitol-building fund, for the use and benefit thereof, the sum of one hundred and fifty thousand dollars.

SEC. 2. The State Treasurer is hereby required to make the transfer on the books of his office made, necessary in section one of this act, and in such a manner that the Capitol-building fund shall stand charged as a debtor to the internal improvement permanent fund as money loaned from that fund to Capitol-building fund, and the faith

of this State is hereby pledged to repay to the internal improvement permanent fund the full amount so loaned, with interest thereon at the rate of three and one-half per cent. per annum from the date of said transfer to the return thereof. The State Treasurer shall also, in writing, notify the State Auditor of such transfer, who shall also make the proper transfer and entry upon the books of his office.

SEC. 3. For the purpose of carrying out the provisions of this act, the State Treasurer is hereby authorized to sell sufficient of the securities in his hands and belonging to the internal improvement permanent fund, the said securities to be sold at not less than par and the accrued interest thereon.

SEC. 4. Whereas in the opinion of the General Assembly an emergency exists; therefore, this act shall take effect and be in force from and after its passage.

Approved April 6, 1891.

AN ACT

TO PROVIDE FOR THE RELIEF OF CERTAIN LABORERS WHO HAVE PERFORMED WORK UPON THE CAPITOL BUILDING OF THE STATE OF COLORADO AND HAVE NOT BEEN PAID THEREFOR.

WHEREAS, One W. D. Richardson, of the State of Illinois, was heretofore the contractor for the erection of the said Capitol building of the State of Colorado; and

WHEREAS, Said Richardson employed certain laborers upon the said Capitol building and certain laborers at the granite quarries near Georgetown, Colorado, in quarrying granite for use in said Capitol building during the year 1887; and

WHEREAS, Said laborers, on account of the failure of said Richardson to comply with his contract and his insolvency, have not been paid for their labor aforesaid. Now, therefore,


Be it enacted by the General Assembly of the State of Colorado:

SECTION 1. That the Board of Capitol Managers of the State of Colorado are hereby authorized, under such regulations as they may adopt, to audit the claims of laborers that have heretofore worked for W. D. Richardson, at Denver, Colorado, in the year of 1877, upon the Capitol building of said State of Colorado, and such laborers as may have worked in the granite quarries at Georgetown, Colorado, for said Richardson in said year, quarrying rock for said building, and to allow each of said laborers the just compensation that may be due to them from said Richardson for such labor, and remaining unpaid; and to pay to each of said laborers, out of the Capitol-building fund, the amount so found due, taking from each of them proper receipts and vouchers for the payment so made. That by such payments the said Board of Capitol Managers shall be subjected to the rights of the parties so paid, and are authorized to collect such sums from the said W. D. Richardson for and in behalf of the State of Colorado.

SEC. 2. There is hereby appropriated out of the Capitol-building fund five thousand (\$5,000) dollars or so much thereof as may be necessary for the purposes contemplated by section 1 hereof.

Approved April 11, 1891.

APPENDIX "H."

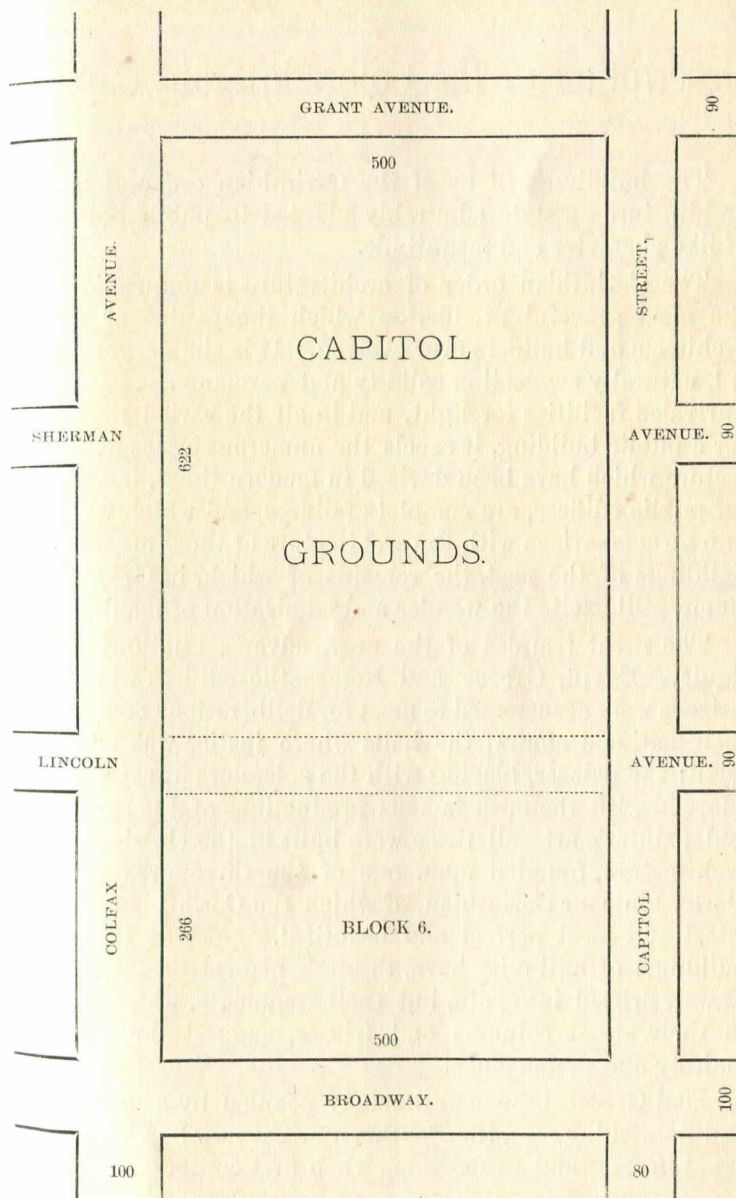

Description of the Colorado State Capitol.

The building will be of the Corinthian order of classic architecture—a style admirably adapted to public buildings of like character and magnitude.

The Corinthian order of architecture is unquestionably the most graceful production which the genius of Greek architects and builders ever evolved. It is simple, yet graceful, naturally suggesting solidity and permanence. It offers unrivaled facilities for light, and in all the varied requisites for a public building, it excels the numerous styles of architecture which have been devised in modern times, but which, for public edifices, are complete failures, and which will sustain no comparison with the architecture of those magnificent buildings of the past, the remains of which, in Greece and Rome, still excite the wonder and admiration of mankind.

The great temples of the most advanced nations of antiquity—Egypt, Greece and Rome—the edifices where the citizens were accustomed to meet for deliberations concerning their national affairs; the halls where justice was administered; the palaces, blazing with the splendors of royalty, and adorned with the most famous productions of the sculptor's and painter's art—all these were built in the classic style of architecture, founded upon one of the three great orders: Doric, Ionic or Corinthian, of which the Corinthian was the latest and most perfect and beautiful. Most of the noted buildings of antiquity have, through neglect or the ravages of war, drifted into ruin, but their fragments, which remain in their silent columns and friezes, suggest the ideas of majesty and permanence.

Had Greece been continuously peopled by a prosperous and flourishing race, the Pantheon might now be viewed as it stood in its grand proportions when first consecrated by the

Athenians; and had the same been true of Egypt, the massive wonders of hundred-gated Thebes might still be seen in their grandeur, and the stately classic temples of Karnak and Luxor. In our advanced American civilization there need be no apprehension that the Capitol building of Colorado will not stand, a handsome and stately structure, the admiration of future ages.

It seems strange that elements so few, though admitting of a great variety of outline, should be capable of producing these exquisite forms of beauty, which will always be the admiration of the civilized world. Yet these features, so simple in their nature, require in their treatment the greatest skill to produce a building of true classic grandeur. Simplicity is peculiar to classic architecture, and is its grand characteristic.

The new Capitol will contain a sub-basement, a full basement, and first, second and third stories, constructed entirely of cut-stone, with surfaces smoothly dressed for all the exterior work above the grade line, and will be surmounted by an elegant dome. The entire workmanship of the four fronts and dome will be strictly Corinthian, having no unnecessary carving, but ornamented simply by the embellishments demanded by the Corinthian order, which, like its two classic sisters, relies for its grand effects upon correct proportions and properly treated details, rather than elaborate and excessive ornamentation. For beauty and utility combined, no other form of architecture can equal the Corinthian, and the value of this and its kindred orders—the Doric and Ionic—will be readily appreciated when the simple and evident fact is considered, that while all other forms of architecture have, within the past two thousand years, undergone modifications, entire changes and utter annihilation, these recognized models continue to exist, as when first designed, the accepted form for stately public buildings, such as the Capitol building for a great State, by right, should be.

The style of architecture for a public building should be suited to the building itself, and the purposes for which it is

intended to be used. Where laws are to be enacted for the government of a great State, public records preserved, and accommodations provided for the executive and judiciary branches of the government, the character of the building should be such as would command respect for these high purposes; and the grotesque and fanciful styles of architecture, resorted to so extensively at the present day, should be carefully shunned as unbecoming to a structure where dignity of appearance is demanded by its uses.

The building will have no useless towers, minarets or turrets, which, while expensive, are of little or no value. They may serve to illustrate or enliven a badly proportioned design, or lead the eye away from violations of harmony, and thereby prove a momentary attraction to the uncultivated, but can never secure the approbation of the cultured student or connoisseur.

In the main pediment will be presented an allegorical group of statuary, representing the wealth, progress and substantial interests of the State of Colorado, and the various channels leading to their development.

VENTILATION.

This most important requisite to a public building has been fully and intelligently provided for. By use of powerful exhaust fans, the foul air will be constantly taken from every portion of the building, and forced directly into the smoke shaft. The vacuum thus produced will be at once supplied with an equal amount of fresh air, taken at a point one hundred and eighty feet above the ground, at the corners of the dome wall, where the air is never contaminated with dust or foul vapors. The air thus received by the use of supply fans is forced through the fresh air ducts to every part of the building, and properly warmed by contact with the direct radiators before its admission into the apartments and corridors.

HEATING.

The building will be heated by steam, generated by four steel boilers, which will be located in the sub-basement.

These boilers will also supply steam for the operation of the pumps in connection with the elevators, and for the operation of the ventilation of the building.

THE SUB-BASEMENT.

In the sub-basement will be located the boilers, engine, exhaust and supply fans, and ample room for the storage of fuel. The fuel room will be reached by an underground passageway from the street, with suitable tracks, so that coal may be brought into the building by this system, thereby avoiding the nuisance of coal dust, which would result should other methods be adopted. Below the sub-basement floor, which will be concreted, will be placed all the foul-air ducts, the steam supply and return lines, together with the drainage and sewerage of the building.

THE BASEMENT.

The basement story will have a clear height of 15 feet, and all of the apartments will be well lighted. It will contain rooms for the Adjutant General, State Geologist and mineral cabinet, Commissioner and Inspector of Mines, Horticultural and Historical societies, storage and vault rooms for Secretary of State, janitor and engineer's living rooms, wash rooms, and water closets.

THE FIRST STORY.

On the first floor will be the apartments of the Governor, Attorney General, Secretary of State, State Auditor, State Treasurer, Railroad Commissioner, Superintendent of Public Instruction, Insurance Commissioner, and State Engineer. All the offices are provided with fireproof vaults, and wardrobe accommodations for most of them. The offices have been arranged and located with especial reference to their business connections with each other, and the convenience not only of the officers who will occupy them, but of those who will have public business transactions therein. The story will have a clear height of twenty-one feet, and will have spacious and well-lighted corridors, extending the entire length and breadth of the building, and crossing at the spacious rotunda in the center.

SECOND STORY.

Upon the second floor are located the Legislative halls, the Supreme Court room, consultation and private rooms of the judges, the State library, Librarian's apartments, Legislative postoffice, and rooms for Legislative officers. The Legislative halls and State library will occupy the height of the second and third stories, as more fully described below. The Representative hall will occupy the west front, being 63 feet in length by 52 feet in width, and having a height of 42 feet. Connected with it are the rooms of the Speaker and Clerk, lobbies, and appropriate cloak and toilet rooms. Private stairs will lead from the consultation rooms to the galleries, which will be on the line of the third story floor. The ceiling of the hall will be coffered and paneled, and the walls surrounding the room will have fluted pilasters with Ionic caps on the floor line, and the same with Corinthian caps on the line of the gallery, with stucco cornices on each line of caps. The Senate chamber is at the south end of the building, and will correspond in height and character of finish with the Representative hall. It will be 64 feet in length by 37 feet in width, and have in connection the rooms required for the officers and committees of the Senate, corresponding with those provided for the House.

The State library—with the Law library adjoining—is located at the east front of the building, also occupying the height of the second and third stories. The State library is 67 feet in length by 50 feet in width, each tier of alcoves being reached by circular iron-stairs from the office of the Librarian. The Law library, adjoining the State library, has a length of 48 feet and a breadth of 32 feet, with two consultation rooms for attorneys adjoining, and forming a direct connection with the Supreme Court room. The Supreme Court room is also located upon the second floor, and has adjoining it private and consultation rooms for the judges, and offices for the clerk and marshal. Connected with the judges' apartments is a fireproof vault, for the deposit of records and other valuable papers.

THE THIRD FLOOR.

The larger portion of this story is taken up by the galleries of the principal apartments already described upon the second floor. The remainder of the story is occupied by committee rooms, offices for engrossing and enrolling, which are admirably adapted to the purpose by the superior light afforded, and rooms for storage.

THE ROTUNDA.

The rotunda will be a magnificent feature of the building, and not only add greatly to its beauty, but will be of great utility also in furnishing an abundance of light to the halls and corridors. It will have a diameter of 45 feet, being open from the basement to the diaphragm of the dome, and having balconies surrounding it on a line with the several floors. The walls of the rotunda will be of a proper finish for fresco ornamentation, and may be suitably decorated at any time, and thereby made more attractive and interesting by representations of the men, or the industries or resources of the State, all of which have combined to place Colorado in the foremost rank of the sisterhood of States. In the walls of the rotunda, on the line of the several balconies, niches and recesses will be provided for the reception of appropriate statuary. Promenades will be provided around the exterior of the dome, and stairways lead from the attic floor to the lantern, affording to the sightseer an unequaled view of the surrounding country.

THE CORRIDORS.

The broad and ample corridors will add largely to the interior beauty of the building. Those of the main floor have beautiful tile floors. On either side of the rotunda rise the grand stairways, constructed entirely of iron.

SKYLIGHTS.

The Legislative halls, the Supreme Court room, the State and Law libraries and the stairways will all be lighted by beautiful stained-glass skylights, the portions of the roof directly over these skylights being of heavy hammered glass, so that an abundance of light is admitted in each place where

it is required. The dome will also have beautiful windows of stained glass.

The building, when completed, will be the finest in the State of Colorado, and one of the finest capitol buildings in the country, of which every citizen of the State may be justly proud.

The following is a further description of the building, with number and sizes of rooms, together with drawings of the several floors, by R. C. Greiner, civil engineer, who laid off the foundations for the first contractor, W. D. Richardson:

DIMENSIONS.		FT.	IN.
North and south		294	4
—Projections, 6 feet 5 inches each		13	10
—Porticoes, 13 feet 5 inches each		26	10
—Approaches, 24 feet 5 inches each		48	11
Extreme length		383	11
East and west—through center of building		230	10
—Porticoes, 13 feet 5 inches each		26	10
—West frontage approaches		32	6
—East frontage approaches		22	10
Extreme width		313	00
<i>Frontages—</i>			
East, Grant avenue		95	2
West, Lincoln avenue		95	2
South, Capitol avenue		160	5
North, Colfax avenue		165	5
Height of building, from grade line to gutter in upper cornice		86	5
Height of building, from concrete to gutter in upper cornice		102	6
Height of west pediment, from grade line to top		92	5
Height of dome, from top of concrete to top of statue		272	2
Height of dome, from grade line to top of statue		256	0
<i>Capacity of State Library—</i>			
Volumes		25,000	
<i>Capacity of Law Library—</i>			
Volumes		13,000	
<i>Basement—</i>			
CORRIDORS.		FT.	
Length, north and south		271	
72 feet south of dome		56	wide
72 feet north of dome		56	wide
36 feet south of dome		36	wide
36 feet north of dome		36	wide
Length, east and west		199	
In center		70x70	
West front		35	wide
East front		15	wide
Circular corridor in dome, diameter		42	

	FT.	
<i>First Story—</i>		
North and south, up to vestibules	272	
72 feet south of dome	56	
72 feet north of dome	56	
36 feet south of dome	37	wide
36 feet north of dome	37	wide
East and west, up to vestibules, length	200	
In center	71x71	wide
West front	36	wide
East front	16	wide
Circular corridor in dome, diameter	43	
<i>Second Story—</i>		
North and south, length	200	
East and west, length	75	
East and west	56	wide
<i>Third Story—</i>		
North and south, length	191	
East and west, length	66	
East and west	56	wide

	FT.	IN.
HEIGHTS OF STORIES.		
Sub-basement	14	6
Basement	15	2
First story	21	0
Second story	21	4
Third story	20	4

NUMBER OF ROOMS IN BUILDING.	
Basement	33 rooms.
First story	45 rooms.
Second story	49 rooms.
Third story	33 rooms.
Total	160 rooms.

ROOMS IN BASEMENT STORY.


No. 3. Secretary of State.....	23 x 43
No. 4. Secretary of State.....	14 x 22
No. 5. Secretary of State.....	14 x 16
No. 6. Secretary of State.....	14 x 20
No. — Secretary of State, wardrobe.....	9 x 9
No. — Secretary of State, vault.....	14 x 24
No. — Secretary of State, vault.....	8 x 11
No. 28. Adjutant General.....	16 x 33
No. 29. Adjutant General.....	32 x 34
No. 30. Adjutant General.....	11 x 31
No. 31. Adjutant General.....	24 x 31
No. 26. Inspector of Mines.....	34 x 31
No. 27. Inspector of Mines.....	32 x 16
No. — Inspector of Mines, wardrobe.....	7 x 10
No. — Inspector of Mines, vault.....	9 x 10
No. 8. Historical Society.....	22 x 54
No. 7. Historical Society.....	21 x 31
No. — Historical Society, wardrobe.....	8 x 9
No. — Historical Society, vault.....	8 x 12
No. 9. Horticultural Society.....	22 x 49
No. 10. Horticultural Society.....	21 x 32
No. — Horticultural Society, wardrobe.....	7 x 7
No. — Horticultural Society, vault.....	13 x 14
No. — Horticultural Society, vault.....	7 x 13
No. 11. State Geologist.....	14 x 20
No. 12. State Geologist.....	14 x 20
No. — State Geologist, store-room.....	9 x 17
No. 13. Mineral Cabinet.....	30 x 41
No. 14. Mineral Cabinet.....	13 x 21
No. 15. Mineral Cabinet.....	10 x 18
No. — Mineral Cabinet, store-room.....	8 x 20
No. — Mineral Cabinet, store-room.....	7 x 19
No. — Mineral Cabinet, wardrobe.....	8 x 10
No. 16. Unassigned offices.....	15 x 18
No. 17. Unassigned offices.....	14 x 20
No. 18. Unassigned offices.....	11 x 26
No. 19. Unassigned offices.....	11 x 20
No. — Unassigned offices, vault.....	6 x 11

ENGINEER'S DEPARTMENT.

No. 1. Boiler room.....	40 x 31
No. 2. —.....	24 x 11
No. 33. —.....	14 x 15
No. 32. —.....	14 x 20
No. —.....	8 x 11
No. —, wardrobe.....	9 x 9
No. —, store-room.....	7 x 14
No. —, store-room.....	11 x 11

JANITOR'S DEPARTMENT.

No. 20. Kitchen.....	20 x 14
No. 21. Dining room.....	12 x 14
No. 22. Sitting room.....	24 x 13
No. 23. Bedroom.....	18 x 17
No. 24. Bedroom.....	17 x 14
No. 25. Bathroom.....	10 x 7
No. — Pantry.....	8 x 9
No. — Store-room.....	8 x 9
No. — Wardrobe.....	5 x 6

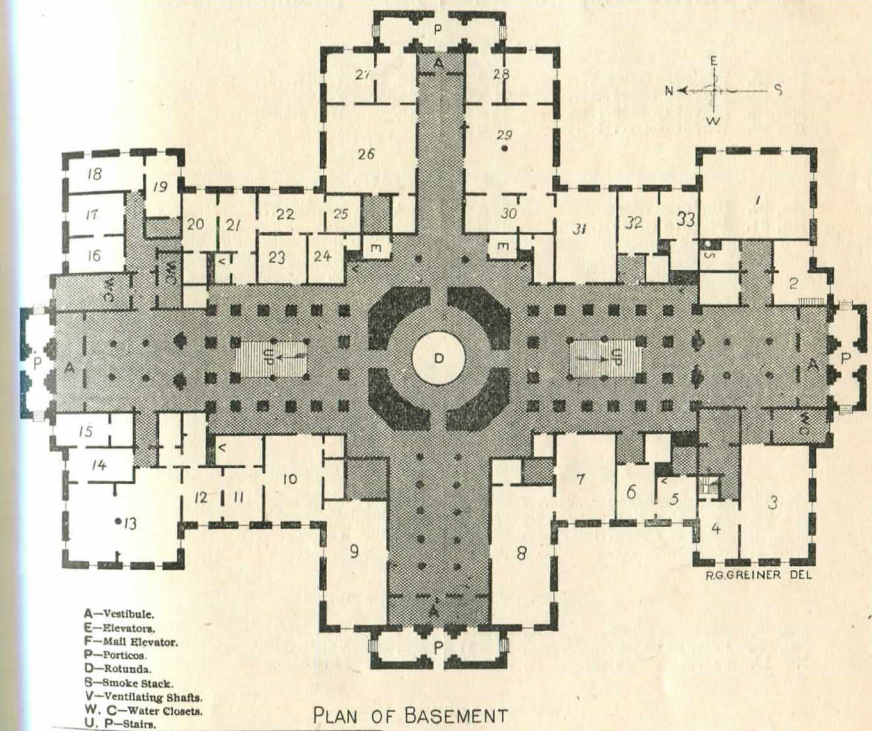

PLAN OF BASEMENT

FIRST STORY.

GOVERNOR.

No. 38. Reception room.....	22 x 54	No. — Wardrobe.....	9 x 10
No. 39. Business office.....	21 x 32	No. — Vault.....	8 x 12
No. 40. Private office.....	14 x 21		

SECRETARY OF STATE.

No. 44. Business office.....	24 x 44	No. 45. Wardrobe.....	11 x 18
No. 42. Private office.....	15 x 22	No. 43. Vault.....	15 x 24
No. 41. Private office.....	15 x 16	No. — Vault.....	9 x 11

STATE TREASURER.

No. 36. Business office.....	22 x 49	No. 37. Vault.....	13 x 15
No. 35. Private office.....	21 x 32	No. — Vault.....	8 x 13
No. 32. Private office.....	14 x 21	No. — Wardrobe.....	7 x 7
No. 33. Wardrobe.....	10 x 17		

AUDITOR OF STATE.

No. 30. Business office.....	32 x 40	No. 34. Vault.....	16 x 20
No. 31. Private office.....	15 x 21		

INSURANCE DEPARTMENT.

No. 29. Business office.....	14 x 21	No. — Wardrobe.....	8 x 11
No. 28. Private office.....	11 x 18		

ATTORNEY GENERAL.

No. 27. General office.....	11 x 20	No. — Wardrobe.....	7 x 11
No. 26. Private office.....	15 x 19		

SUPERINTENDENT OF PUBLIC INSTRUCTION.

No. 17. Business office.....	28 x 32	No. 20. Wardrobe.....	8 x 10
No. 18. Private office.....	15 x 20	No. 19. Wardrobe.....	9 x 10
No. 22. Private office.....	15 x 20	No. 16. Vault.....	10 x 11
No. 21. Wardrobe.....	9 x 10		

BOARD OF LAND COMMISSIONERS.

No. 8. Business office.....	32 x 35	No. 7. Wardrobe.....	10 x 12
No. 9. Private office.....	17 x 17	No. — Vault.....	11 x 19
No. 10. Private office.....	15 x 17	No. 6. Map room.....	26 x 32

RAILROAD COMMISSIONERS.


No. 13. Business office.....	31 x 35	No. 14. Wardrobe.....	8 x 11
No. 12. Private office.....	15 x 17	No. 15. Vault.....	10 x 11
No. 11. Private office.....	16 x 17		

STATE ENGINEER.

No. 1. Business office.....	31 x 40	No. 4. Private office.....	15 x 16
No. 2. Wardrobe.....	11 x 12	No. 5. Private office.....	15 x 21
No. 3. Vault.....	18 x 25	No. — Wardrobe.....	9 x 10


UNASSIGNED OFFICES.

No. 23. _____.....	14 x 20	No. 25. _____.....	12 x 21
No. 24. _____.....	12 x 27	No. — Vault.....	7 x 11

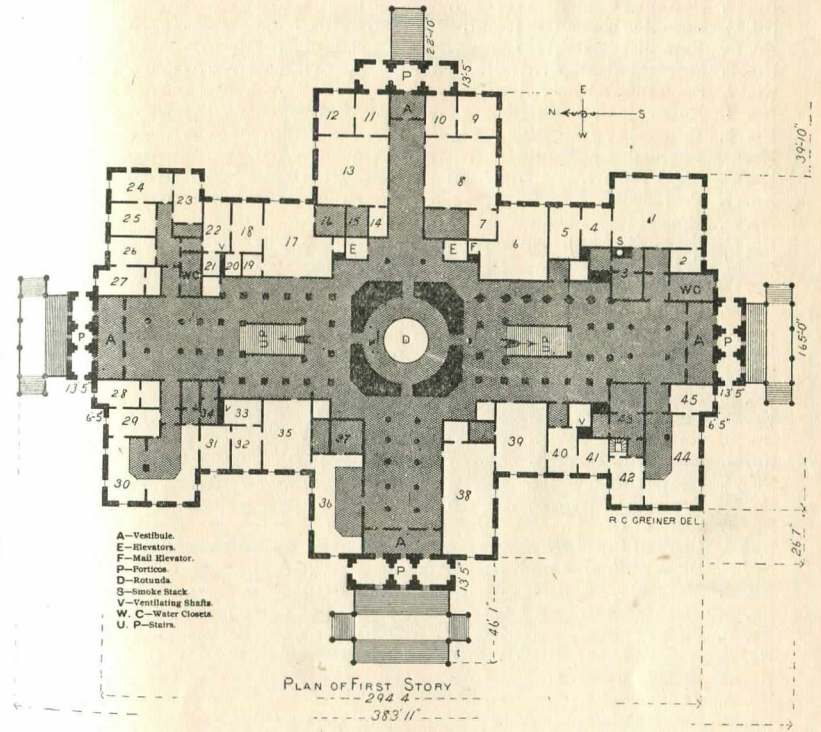

SECOND STORY.

No. 8.	Senate chamber.....	37 x 64
No. 7.	Senators' consultation room.....	11 x 23
No. 6.	Senators' consultation room.....	11 x 25
No. 5.	Senators' consultation room.....	11 x 14
No. 9.	Secretary of Senate.....	11 x 17
No. 10.	Secretary of Senate.....	17 x 18
No. 11.	Lieutenant Governor and President of Senate.....	13 x 24
No. 12.	Lieutenant Governor and President of Senate.....	15 x 23
No. 13.	Enrolling committee room.....	15 x 16
No. 14.	Enrolling committee room.....	15 x 21
No. 15.	Enrolling committee room.....	21 x 32
No. 3.	Sergeant-at-Arms.....	17 x 18
No. 4.	Sergeant-at-Arms.....	16 x 17
No. 1.	Engrossing committee.....	13 x 24
No. 2.	Engrossing committee.....	16 x 18
No. 49.	Engrossing committee.....	19 x 18
No. 48.	Cloak room.....	15 x 21
No. 47.	Post-office.....	18 x 22
No. 23.	House of Representatives.....	52 x 63
No. 16.	Sergeant-at-Arms.....	13 x 23
No. 17.	Sergeant-at-Arms.....	10 x 19
No. 18.	Chief Clerk.....	12 x 22
No. 19.	Chief Clerk.....	11 x 12
No. 20.	Speaker's room.....	10 x 15
No. 21.	Speaker's room.....	11 x 12
No. 22.	Members' consultation.....	12 x 22
No. 24.	Members' consultation.....	10 x 17
No. 25.	Cloak room.....	13 x 23
No. 26.	Engrossing rooms.....	21 x 22
No. 27.	Engrossing rooms.....	15 x 21
No. 28.	Engrossing rooms.....	14 x 21
No. 32.	Supreme Court.....	46 x 63
No. 31.	Clerk of Court.....	14 x 21
No. 30.	Clerk of Court.....	15 x 29
No. —	Clerk of Court's vault.....	— x —
No. 29.	Marshal.....	11 x 24
No. 33.	Judge's room.....	15 x 19
No. 34.	Judge's room.....	14 x 20
No. 35.	Judge's room.....	13 x 26
No. 36.	Judge's room.....	12 x 20
No. 37.	Judge's room.....	15 x 21
No. 38.	Judge's room.....	15 x 21
No. 39.	Consultation room.....	17 x 26
No. 40.	Attorney's consultation room.....	14 x 30
No. 41.	Law library.....	32 x 48
No. 42.	State library.....	50 x 67
No. 43.	Private rooms.....	15 x 17
No. 44.	Private rooms.....	16 x 17
No. 45.	Librarian's rooms.....	14 x 14
No. 46.	Librarian's rooms.....	13 x 25

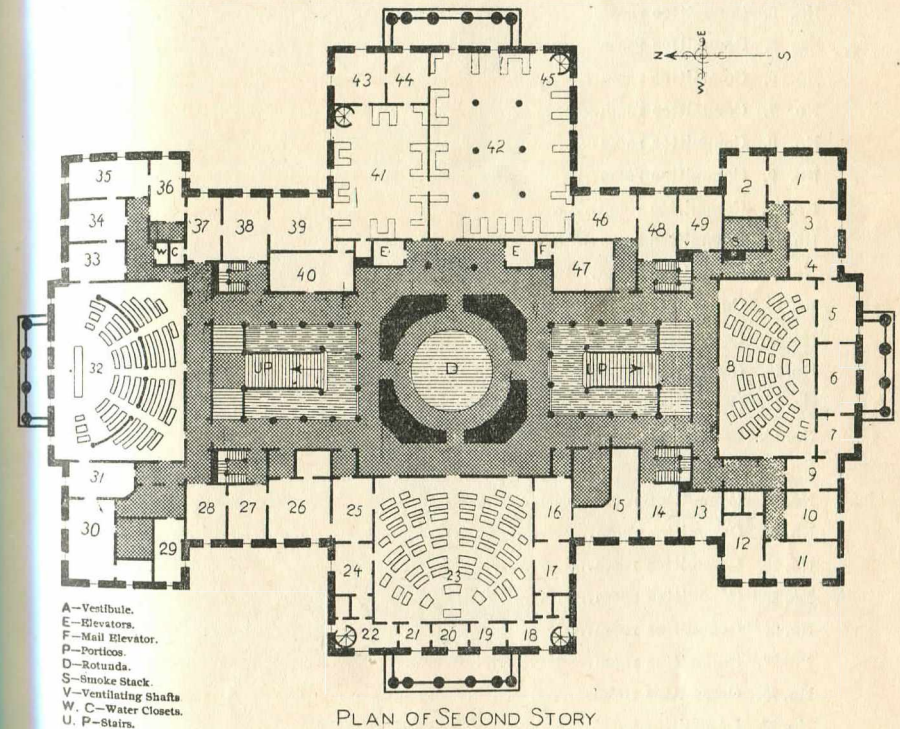

PLAN OF SECOND STORY

THIRD STORY.

No. 4.	Gallery of Senate.	
No. 12.	Gallery of House of Representatives.	
No. 29.	Gallery of Library.	
No. 1.	Committee room.....	14 x 24
No. 2.	Committee room.....	16 x 18
No. 3.	Committee room.....	17 x 17
No. 5.	Committee room.....	16 x 17
No. 6.	Committee room.....	13 x 24
No. 7.	Committee room.....	16 x 23
No. 8.	Committee room.....	12 x 15
No. 9.	Committee room.....	12 x 15
No. 10.	Committee room.....	15 x 22
No. 11.	Committee room.....	12 x 16
No. 13.	Committee room.....	21 x 22
No. 14.	Committee room.....	15 x 21
No. 15.	Committee room.....	15 x 21
No. 16.	Committee room.....	12 x 22
No. 17.	Committee room.....	15 x 29
No. 18.	Committee room.....	14 x 22
No. 19.	Committee room.....	15 x 17
No. 20.	Committee room.....	14 x 12
No. 21.	Committee room.....	13 x 27
No. 22.	Committee room.....	13 x 21
No. 23.	Committee room.....	15 x 22
No. 24.	Committee room.....	15 x 22
No. 25.	Committee room.....	18 x 25
No. 26.	Committee room.....	14 x 23
No. 27.	Committee room.....	15 x 18
No. 28.	Committee room.....	16 x 18
No. 30.	Committee room.....	13 x 25
No. 31.	Committee room.....	18 x 22
No. 32.	Committee room.....	12 x 15
No. 33.	Committee room.....	12 x 15

